



West Valley-Mission Community College District

Board of Trustees Meeting Measure W Bond Program Update July 18, 2023

Presented by:
Terrance DeGray, PE, CCM
ASSOCIATE VICE CHANCELLOR
FACILITIES DEVELOPMENT AND OPERATIONS



West Valley - Mission

Community College District

Presentation Overview

1. Measure W Summary
2. Escalation Impacts from 2018 to Current
3. Cost Control Measures
4. Project Delivery Methods
5. Q&A



Measure W Bond Program Timeline

On Nov. 6, 2018, voters passed Measure W in the amount of \$698 million.

1. Measure W is planned as a 12-year program with 4 bond issues.
 1. In April 2019, the first issuance of \$100 million was sold.
 2. In April 2022, the second issuance of \$200 million will be sold.
 3. In April 2025, the third issuance of \$200 million will be sold.
 4. In April 2028, the fourth issuance of \$148 million will be sold.
2. Measure W is about 17% complete.



Measure W Bond Allocation

Measure W (Voter approved Nov. 6, 2018)

District Services	\$162.7 Million
Mission College	\$266.5 Million
West Valley College	\$268.8 Million
Total: \$698 Million	



DISTRICT SERVICES PROJECT LIST

Project	Current Budget	Expenditures	Encumbrances	Balance	% Complete
ADA Barrier Removal	\$ 3,915,000	\$ 625,028	\$ 33,833	\$ 3,256,139	16%
Administration Building Upgrades	\$ 12,685,195	\$ 607,787	\$ -	\$ 12,077,408	5%
Alternative Energy Project	\$ 31,526,000	\$ 27,125,579	\$ 4,332,894	\$ 67,527	86%
Fire Alarm Upgrades	\$ 3,262,500	\$ 9,871	\$ 9,500	\$ 3,243,129	0%
HVAC/Lighting Energy Retrofit	\$ 9,000,000	\$ 318,127	\$ 76,330	\$ 8,605,543	4%
IS Server & Infrastructure Upgrd	\$ 8,482,500	\$ 1,910,046	\$ 53,543	\$ 6,518,911	23%
ParkingLot/Road/Sidewalk Repl	\$ 15,265,000	\$ 1,228,226	\$ 170,336	\$ 13,866,438	8%
Police Parking & Storage Fac	\$ -	\$ -	\$ -	\$ -	0%
Program Contingency	\$ 10,355,855	\$ 388,642	\$ 89,032	\$ 9,878,182	4%
Program Management	\$ 12,276,850	\$ 3,909,356	\$ 39,064	\$ 8,328,430	32%
Public Safety & Comm Srv Bldg	\$ 16,563,600	\$ 1,734,801	\$ 11,129,098	\$ 3,699,701	10%
Security, Safety & Monitoring	\$ 3,870,000	\$ 473,826	\$ 567,147	\$ 2,829,027	12%
Storm Water MP & Implement	\$ 6,525,000	\$ 374,336	\$ 141,324	\$ 6,009,340	6%
Undergrnd Water & Sewer Upgrd	\$ 14,915,000	\$ 905,081	\$ 149,748	\$ 13,860,171	6%
Utility/Electrical Bldg Upgrd	\$ 12,050,000	\$ 1,548,792	\$ 172,683	\$ 10,328,525	13%
Vasona Creek Improvements	\$ 2,007,500	\$ 1,934,133	\$ 44,088	\$ 29,279	96%
Grand Total	\$ 162,700,000	\$ 43,093,631	\$ 17,008,621	\$ 102,597,748	26%



WEST VALLEY COLLEGE PROJECT LIST

Project	Current Budget	Expenditures	Encumbrances	Balance	% Complete
Athletic Field Turf Restoration WV		\$ -	\$ -	\$ -	0%
Black Box Theater - New Building WV	\$ 1,636,800	\$ -	\$ -	\$ 1,636,800	0%
Fine Arts & Music New Building WV	\$ 23,602,700	\$ 2,343,190	\$ 1,972,282	\$ 19,287,228	10%
Fine Arts Replacement Bldg WV	\$ 12,199,000	\$ 10,835,753	\$ 1,318,199	\$ 45,048	89%
Landscape and Gateway Additions WV	\$ 11,343,100	\$ 2,551,176	\$ 194,784	\$ 8,597,140	22%
Learning Resource Ctr Ren WV	\$ 18,836,000	\$ 3,938,398	\$ 12,240,406	\$ 2,657,196	21%
Modular Removal Site Restoration WV	\$ 1,265,100	\$ 616,908	\$ -	\$ 648,192	49%
Outdoor Clsrn & Perf. Space Add. WV	\$ 2,108,600	\$ -	\$ -	\$ 2,108,600	0%
Outdoor PE Facilities Upgrades WV	\$ 29,506,300	\$ 26,793,387	\$ 2,369,905	\$ 343,008	91%
Program Contingency WV	\$ 13,006,000	\$ -	\$ -	\$ 13,006,000	0%
Signage & Wayfinding Master Plan WV	\$ 1,497,400	\$ 277,945	\$ 10,001	\$ 1,209,454	19%
Swing Space for Bldg Proj WV	\$ 2,252,800	\$ 1,299,396	\$ 103,548	\$ 849,856	58%
Theater Renovation and Expansion WV	\$ 29,729,200	\$ 1,781,669	\$ 2,732,144	\$ 25,215,387	6%
Wellness Center - New Building WV	\$ 74,379,400	\$ -	\$ -	\$ 74,379,400	0%
Admin Building Reovation - Repurpose	\$ 5,156,200	\$ -	\$ -	\$ 5,156,200	0%
Campus Center Upgrades	\$ 1,265,100	\$ -	\$ -	\$ 1,265,100	0%
CDC Renovation	\$ 4,029,500	\$ -	\$ -	\$ 4,029,500	0%
General Ed Facilities Augmentation/Upgrd	\$ 3,326,700	\$ -	\$ -	\$ 3,326,700	0%
Guirlani Demo & Site Restoration	\$ 1,921,200	\$ -	\$ -	\$ 1,921,200	0%
Pathway and Bridge Updates	\$ 1,874,400	\$ -	\$ -	\$ 1,874,400	0%
PE/Gym Buildings Renovation	\$ 17,636,300	\$ -	\$ -	\$ 17,636,300	0%
STEM Classroom Expansion & Upgrade	\$ 12,228,200	\$ -	\$ -	\$ 12,228,200	0%
Grand Total	\$ 268,800,000	\$ 50,437,822	\$ 20,941,270	\$ 197,420,908	19%




MISSION COLLEGE PROJECT LIST

Project	Current Budget	Expenditures	Encumbrances	Balance	% Complete
STEM Center New Building MC	\$ 72,244,800	\$ -	\$ -	\$ 72,244,800	0%
Childcare Dev Center Renovation MC	\$ 10,043,200	\$ 8,927,683	\$ 394,146	\$ 721,371	89%
Landscaping & Gateway Additions MC	\$ 9,880,200	\$ 4,208,752	\$ 342,618	\$ 5,328,830	43%
Library Renovation MC	\$ 18,523,800	\$ 2,549,987	\$ 1,987,762	\$ 13,986,051	14%
Modular Removal Site Restoration MC	\$ 3,704,400	\$ -	\$ -	\$ 3,704,400	0%
MT Replacement Bldg MC	\$ 3,287,000	\$ 3,164,918	\$ 168,384	\$ (46,302)	96%
Outdoor Clrm & Perf. Space Add. MC	\$ 3,088,800	\$ -	\$ -	\$ 3,088,800	0%
Outdoor PE Facilities Upgrades MC	\$ 19,758,600	\$ 4,806,411	\$ 0	\$ 14,952,189	24%
Performing Arts Building MC	\$ 46,015,200	\$ 3,102,403	\$ 3,546,102	\$ 39,366,695	7%
Program Contingency MC	\$ 21,913,000	\$ -	\$ -	\$ 21,913,000	0%
Signage & Wayfinding Master Plan MC	\$ 2,469,600	\$ -	\$ -	\$ 2,469,600	0%
Storage and Recycling Facilities MC	\$ 5,191,200	\$ -	\$ -	\$ 5,191,200	0%
Swing Space Renovation Projects MC	\$ 4,321,800	\$ 499,594	\$ 33,199	\$ 3,789,008	12%
General Ed Facilities Augmentation/Upgrd	\$ 3,088,800	\$ -	\$ -	\$ 3,088,800	0%
Science Building Renovation - Repurpose	\$ 19,837,800	\$ -	\$ -	\$ 19,837,800	0%
Student Campus Center Renovation	\$ 19,229,400	\$ -	\$ -	\$ 19,229,400	0%
TAV Building Renovation	\$ 3,902,400	\$ -	\$ -	\$ 3,902,400	0%
Grand Total	\$ 266,500,000	\$ 27,259,748	\$ 6,472,211	\$ 232,768,041	10%

FACILITY MASTER PLANS



Mission College

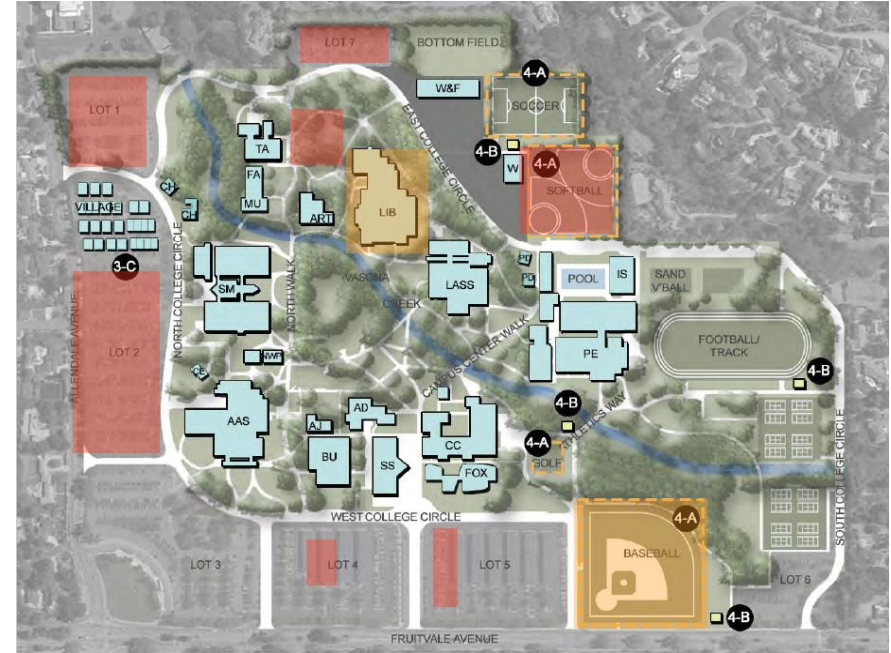

West Valley College

Jun 1, 2023



MEASURE W PROJECTS IN PROGRESS

- WVC FINE ARTS NEW BUILDING
- MOVE-IN ANTICIPATED FALL 2023





MEASURE W PROJECTS IN PROGRESS

- WVC LEARNING RESOURCE CENTER RENOVATION
- CONSTRUCTION START:
 - FEB. 2023
- FUNDING: MEASURE W AND STATE FUNDS

May 26, 2023 at 1:02

Santa Clara

MEASURE W PROJECTS IN PROGRESS



- MC CDC RENOVATION
- ANTICIPATED MOVE IN: FALL 2023

Jun 29, 2023 at 11:10

Santa Clara

Mission

MEASURE W PROJECTS IN PROGRESS



- MC PLAZA COMPLETION
- ANTICIPATED COMPLETION:
AUGUST 2023



MEASURE W PROJECTS IN PROGRESS

- WVC THEATER RENOVATION
- AWAITING DSA APPROVAL
- FUNDING: MEASURE W
AND STATE FUNDS



RIOR VIEW

WVC PERFORMING ARTS CENTER
DESIGN RECAP - 10.10.2024



MEASURE W PROJECTS IN PROGRESS

- WVC MUSIC BUILDING
- AWAITING DSA APPROVAL



MEASURE W PROJECTS IN PROGRESS

- MC LIBRARY RENOVATION
- AWAITING DSA APPROVAL






MEASURE W PROJECTS IN PROGRESS

- MC PERFORMING ARTS CENTER (PAC)
- AWAITING DSA APPROVAL
- FUNDING: MEASURE W AND STATE FUNDS





Annual Escalation Chart

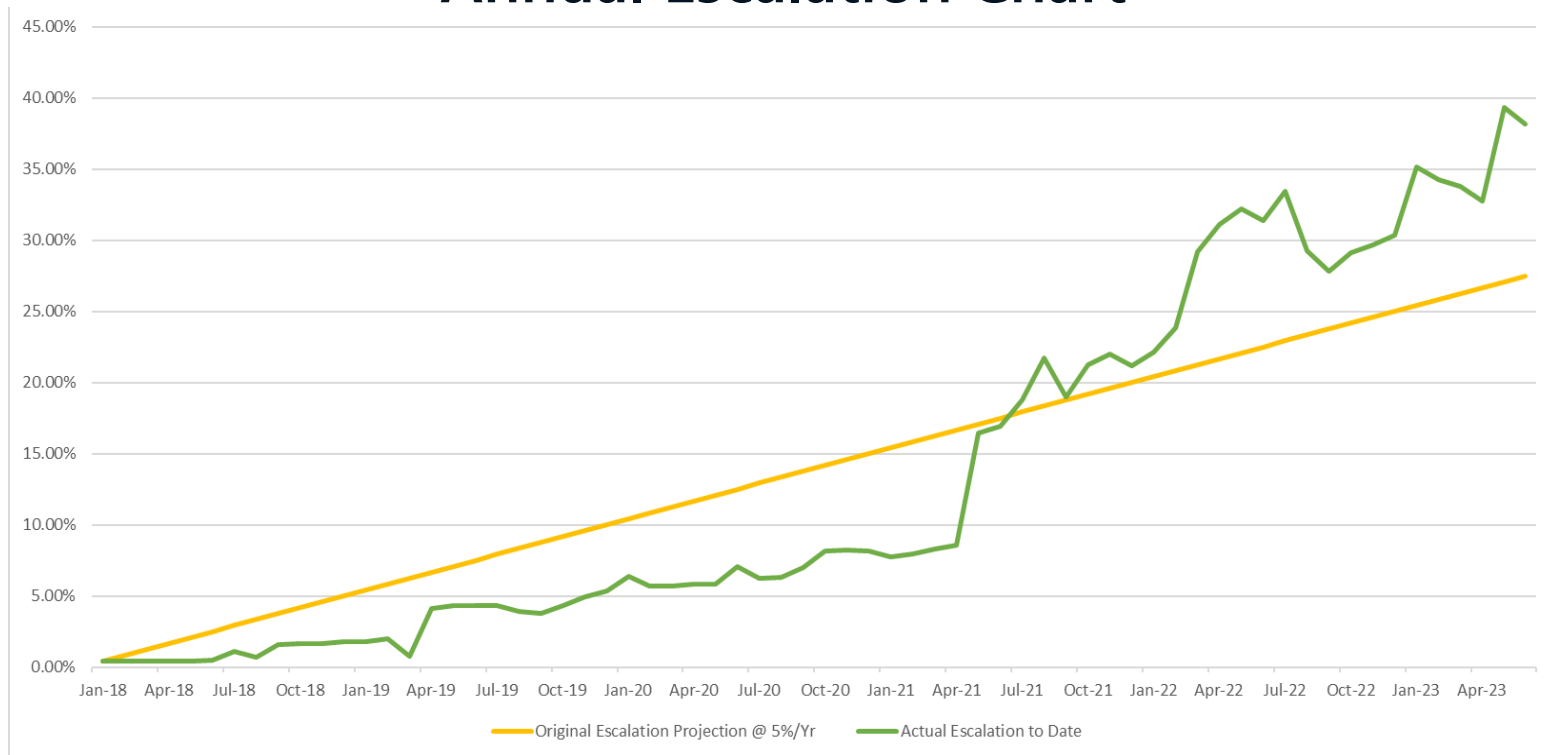

Reference: ENR Construction Cost Index



COST CONTROL MEASURES

- Preconstruction - constructability review
- Design progress estimates
- Value Engineering
- Owner Timely Decisions and Feedback
- Schedule Management
- Total Project Cost Planning
- Risk Management
- Owner Furnished (OFOI / OFCI) Material Procurement
- Alternate Delivery Methods



DELIVERY METHODS

**What Project
Delivery System?**

**What Procurement
Method?**

**What Contract
Format?**

Project Delivery Systems

Design-Bid-Build (DBB)
CM Multi-Prime (MP)
Lease-Lease Back (LLB)
Traditional Design-Build
Progressive Design-Build

Procurement Methods

Best Value
Low Bid
Negotiated
Qualifications-Based
Sole Source (or Direct
Select)

Contract Formats

Cost Plus Fee
Guaranteed Maximum Price (GMP)
Lump Sum (or Fixed Price)
Unit Price



Design-Bid-Build

Under Design-Bid-Build, plans and specifications are completed by an architect and then advertised for bid. Contractors bid the project exactly as it is designed, and the project is awarded to the lowest responsive, responsible bidders. The design consultant team is selected separately and reports directly to the District. The District retains all of the contracts.

Design

Architect designs building in detail and produces complete set of bidding documents

Bid

District publically bids construction documents and awards to lowest responsive and responsible bidder


Build

General Contractor builds project based on construction documents. Errors and omissions are addressed by change order.



Design-Bid-Build

CONTRACT STRUCTURE

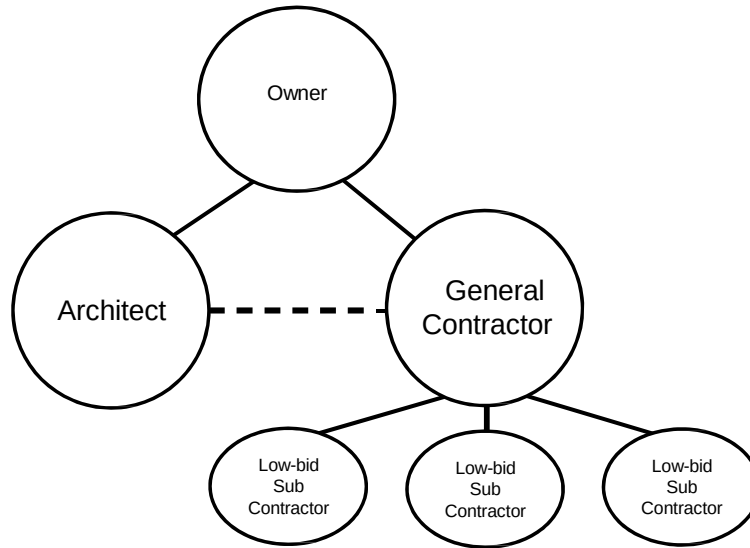

Size	Small	●	●	●	●	●	●	●	Large
Schedule	Simple	●	●	●	●	●	●	●	Complex
Site	Simple	●	●	●	●	●	●	●	Complex
Quality	Standard	●	●	●	●	●	●	●	Landmark
Control	Low	●	●	●	●	●	●	●	High

PROS

- › Most common delivery method
- › Owner maintains control of project through Design

CONS

- › Sequential relationship between design, bidding, and construction can lengthen project schedule
- › Construction cost established after DSA approval
- › Cost overruns or schedule changes can create adversarial relationships between the owner, builder, and designer
- › Greatest risk of general/subcontractor failure
- › Greatest risk of schedule overrun



CM Multi-Prime


CM Multi-Prime provides the District greater flexibility than Design/Bid/Build in selecting the firm which is ultimately responsible for delivering the project. During design, the District awards a contract to a construction management firm (CM), which is selected based on qualifications. The CM does not typically perform any construction work, but manages the project for the District. Under CMMP delivery, the District awards numerous contracts to specific trade contractors on a low-bid basis. The District retains all of the contracts..





CM Multi-Prime

CONTRACT STRUCTURE

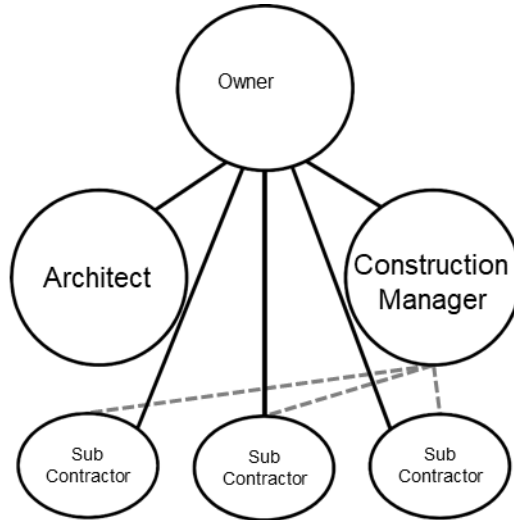

Size	Small	•	•	•	•	•	•	•	Large
Schedule	Simple	•	•	•	•	•	•	•	Complex
Site	Simple	•	•	•	•	•	•	•	Complex
Quality	Standard	•	•	•	•	•	•	•	Landmark
Control	Low	•	•	•	•	•	•	•	High

PROS

- › Efficient delivery method for small/simple projects
- › Owner controls project from design through construction
- › Owner may contract with a construction manager to oversee prime contractors


CONS

- › Overhead costs can escalate, because each prime contractor has overhead that cannot be shared, i.e.: insurance premiums, trailers, scaffolding, etc.
- › Heavy administrative burden
- › Owner accepts risk of all contracts and construction coordination



CM Multi-Prime


IMPACT ON DISTRICT STAFF

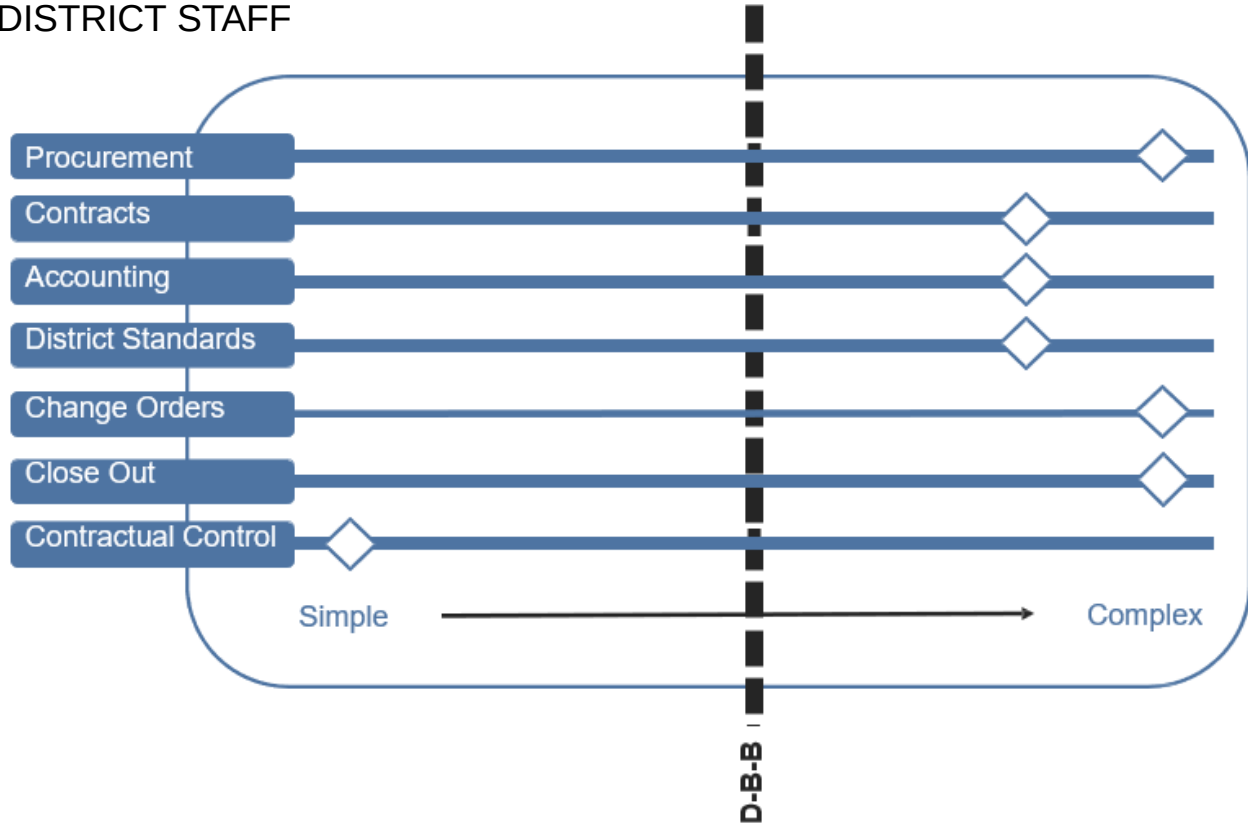



Lease-Leaseback


Lease-leaseback projects allow Districts, without advertising for bids, to lease property currently owned by the District to any lease leaseback agent for a predetermined lease period, which must exceed the construction duration. Selection is based on a best value selection, combining price and qualifications. After the lease period, the buildings vest to the District. This statutory language requires that the District lease its property to a chosen design/build contractor.

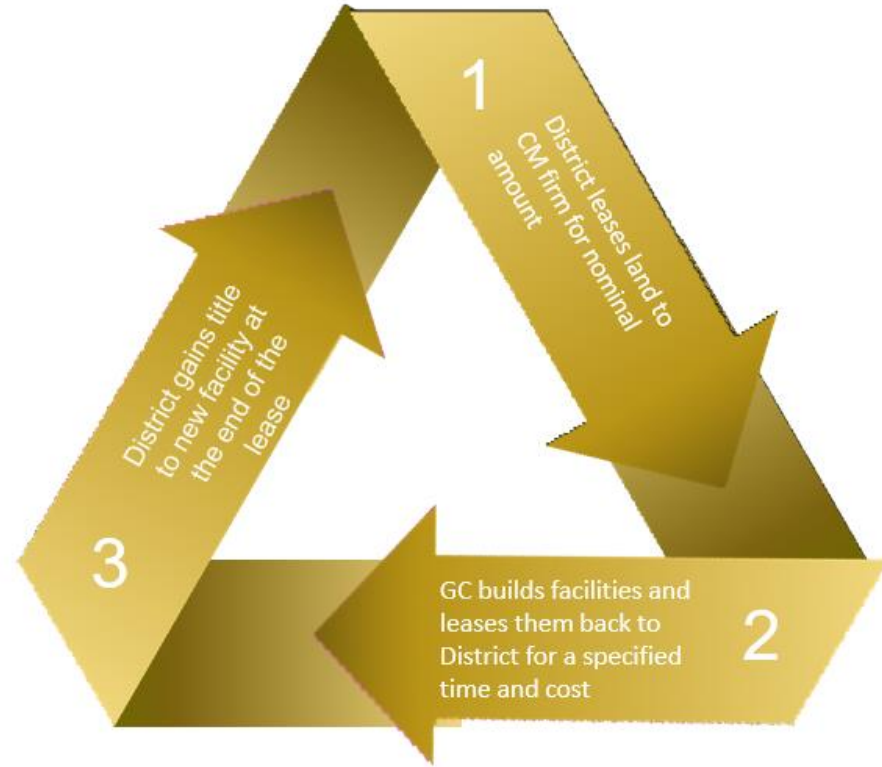



Lease-Leaseback

CONTRACT STRUCTURE

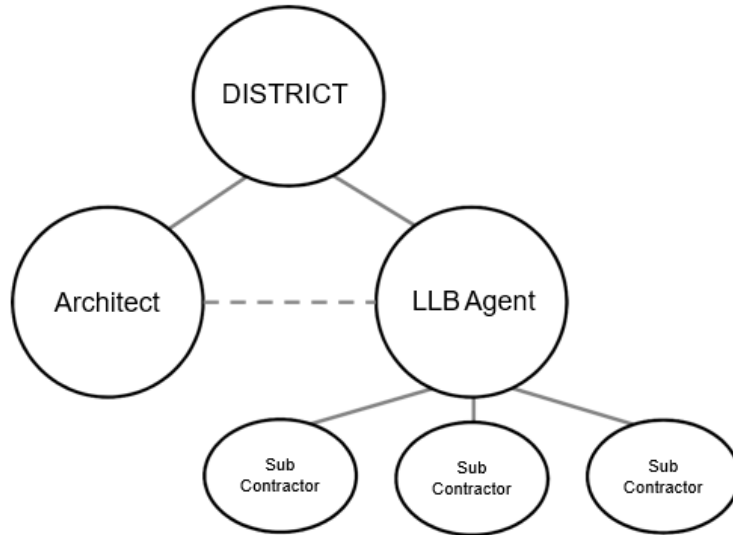

Size	Small	●	●	●	●	●	●	●	●	Large
Schedule	Simple	●	●	●	●	●	●	●	●	Complex
Site	Simple	●	●	●	●	●	●	●	●	Complex
Quality	Standard	●	●	●	●	●	●	●	●	Landmark
Control	Low	●	●	●	●	●	●	●	●	High

PROS

- › LLB Agent is chosen based on best value
- › LLB Agent provides design assist
- › Subcontractors selectively bid
- › LLB Agent maintains facility during the lease period
- › Subcontractors can be chosen for quality and reliability, rather than for lowest cost


CONS

- › Overall cost can be higher
- › Guaranteed Maximum Price (GMP) is negotiated after DSA approval



Lease-Leaseback


IMPACT ON DISTRICT STAFF

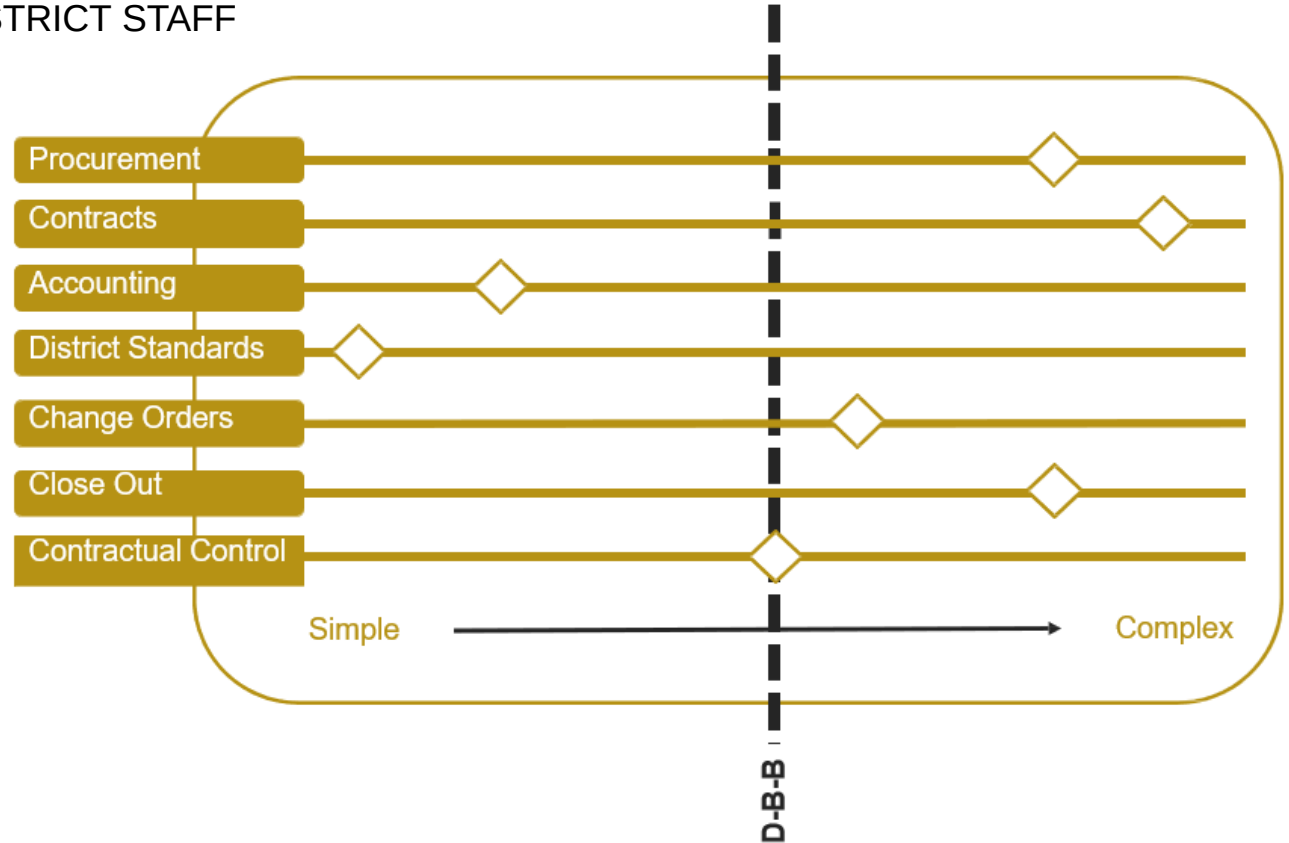



Design-Build


In a Design-Build project, the contractor and architect form a single entity (DBE) to deliver a complete project based on a conceptual plan provided by the District. This method allows for greater control over the schedule, quality of work, and the efficiency of the project as conflicts between design and construction are significantly reduced. The District holds one contract with the DBE, and the DBE holds all subcontractor contracts.

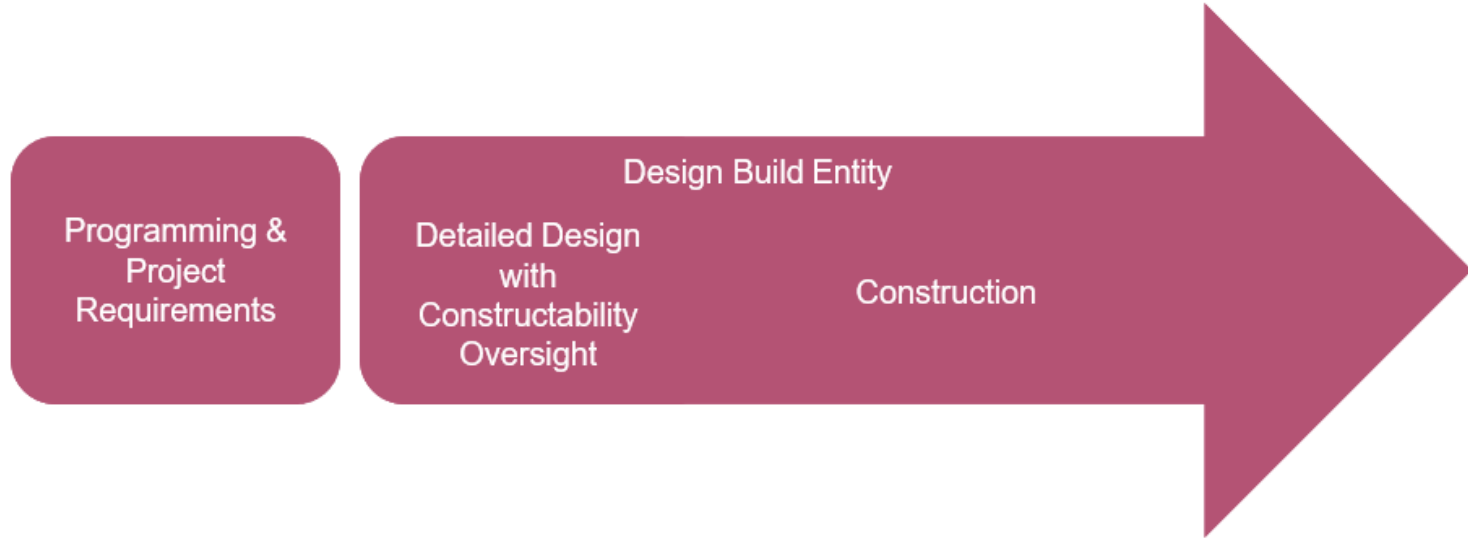



Traditional Design-Build

CONTRACT STRUCTURE

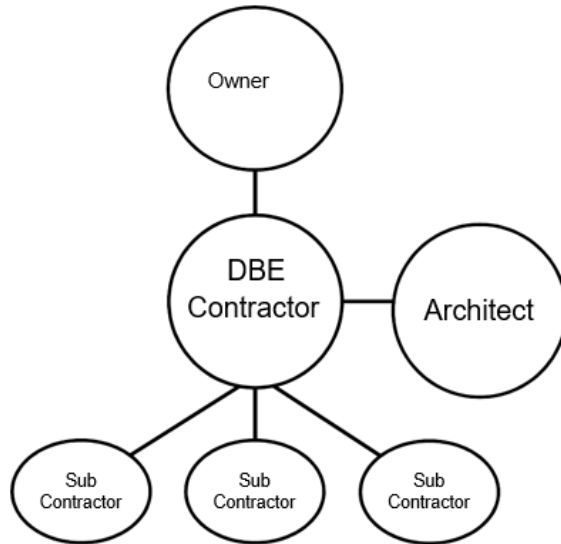

Size	Small	●	●	●	●	●	●	●	Large
Schedule	Simple	●	●	●	●	●	●	●	Complex
Site	Simple	●	●	●	●	●	●	●	Complex
Quality	Standard	●	●	●	●	●	●	●	Landmark
Control	Low	●	●	●	●	●	●	●	High

PROS

- › Design-build entities can be chosen by design competition or chosen by qualifications
- › Guaranteed Maximum Price (GMP) determined prior to construction
- › Risk can be transferred to the design-build entity earlier in design
- › Current legislation requires 60% skilled labor
- › Collaborative relationship between contractor and architect

CONS

- › Complex contractual relationship
- › Architect is hired by the contractor, not the district
- › Some contracts allow the owner less design control



Progressive Design-Build

Similar to Traditional Design-Build project, in that the contractor and architect form a single entity (DBE) to deliver a complete project based on a conceptual plan provided by the District.

Traditional Design Build Process

- 1) Architect develops criteria documents or bridging documents
- 2) Issue RFQ and RFP to select Design-Build Entity
- 3) DBE recommended to the BOT for GMP
- 4) DBE begins design


Progressive Design Build Process

- 1) District develops criteria
- 2) RFQ / RFP for Best Value
- 3) DBE recommended to the BOT for Phase 1 (Preliminary Design / PreCon)
- 4) Design Completed with College/District Input
- 5) Upon Design Completion DBE completes bidding of all trade packages
- 6) District staff prepare recommendation to the BOT for Phase 2 (Construction Services)



Progressive Design Build

IMPACT ON DISTRICT STAFF

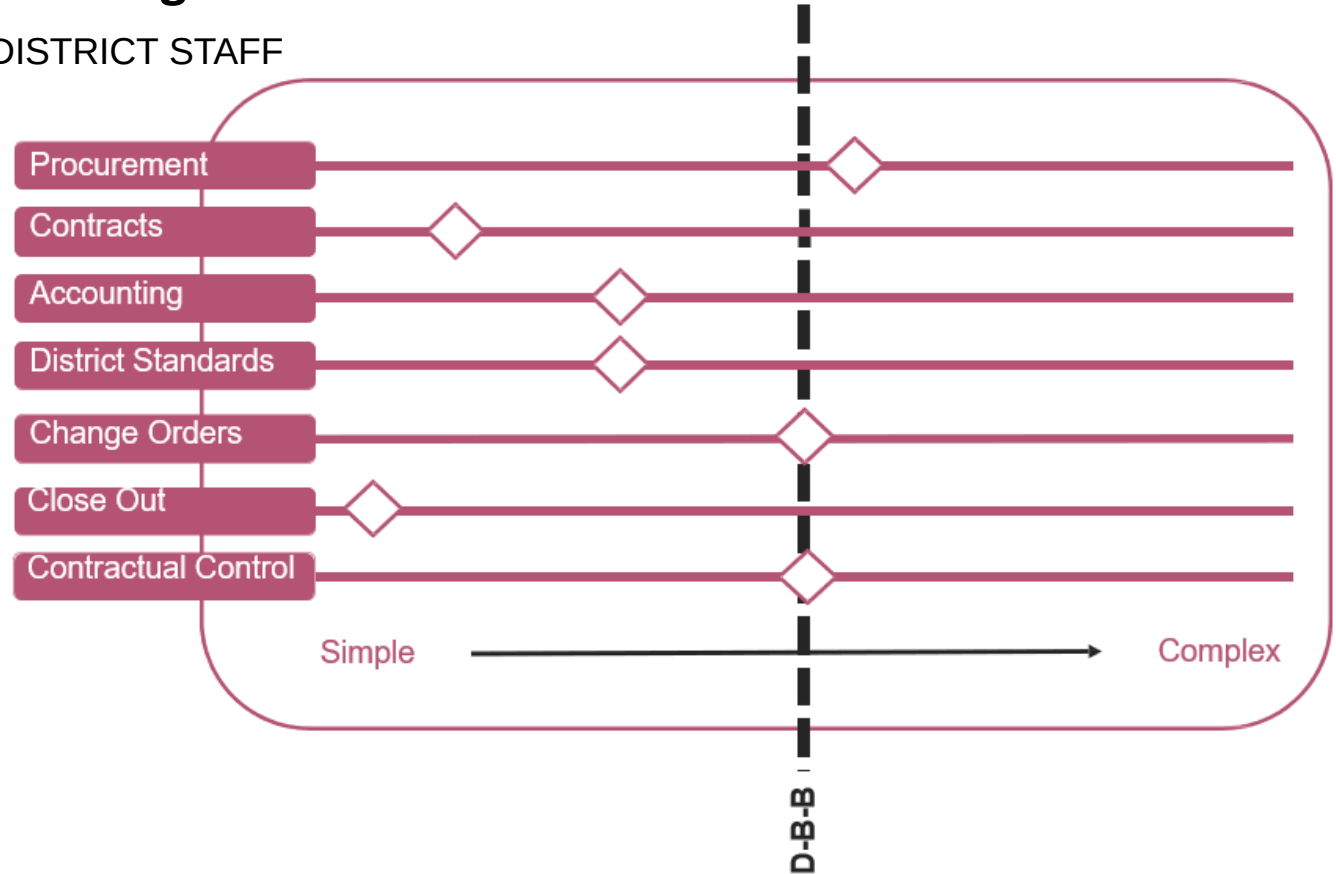



Why Utilize Progressive Design-Build?

- District Has More Influence on Design After Contract Award
- Improved Integrated Design Process
- Leverage Integrated Project Delivery (IPD) and Lean Construction Practices
- Streamlines and simplifies the procurement process, which encourages competition and has a schedule benefit to the project.
- GMP offers the owner transparency into the design- builder's proposal cost (including the pricing for risk and contingencies) and the ultimate cost for final design and construction.
- Provides a collaborative way to establish “single point of responsibility” and eliminate an owner's Spearin Doctrine liability risk.
- Preconstruction services allow
- Reduction in Construction Management staff soft costs



CLOSING REMARKS

Q&A
