

Final Project Proposal

2026-27

Community College Construction Act of 1980 Capital Outlay Budget Change Proposal

Student Campus Center Renovation

Proposal Name

West Valley - Mission Community College District

Community College District

Mission College

College or Center

July 1, 2024

Date

Final Project Proposal Checklist

District:	West Valley Mission Community College District
College/Center:	Mission College
Project:	Student Campus Center Renovation
Prepared by:	ALMA Strategies
Date:	7/1/2024

Section	Description	Status	Date
1.1	Title Page	Complete	7/1/2024
2.1	Final Project Proposal Checklist	Complete	7/1/2024
3.1	Approval Page - Final Project Proposal (with original signatures)	TBD	TBD
3.2	Project Terms and Conditions	Complete	7/1/2024
4.1	Analysis of Building Space Use and WSCH - JCAF 31	Complete	7/1/2024
5.1	Cost Estimate Summary - JCAF 32	Complete	7/1/2024
5.2	Quantities and Unit Costs supporting the JCAF 32	Complete	7/1/2024
6.1	Board of Governors Energy and Sustainability Policy	Complete	7/1/2024
7.1	Responses to Specific Requirements – State Administrative Manual	Complete	7/1/2024
8.1	California Environmental Quality Act	Complete	7/1/2024
9.1	Analysis of Future Costs	Complete	7/1/2024
10.1	Campus Plot Plan	Complete	7/1/2024
10.2	Site Plan	Complete	7/1/2024
10.3	Floor Plans	Complete	7/1/2024
10.4	Exterior Elevations	Complete	7/1/2024
10.5	Electrical Plans <i>(as needed)</i>	N/A	N/A
10.6	Mechanical Plans <i>(as needed)</i>	N/A	N/A
11.1	Guideline-Based Group II Equipment Cost Estimates - JCAF 33	Complete	7/1/2024
12.1	Justification of Additional Costs exceeding Guidelines <i>(as needed)</i>	Complete	7/1/2024
13.1	Detailed Equipment List ^{1/}	N/A	N/A

1/ Traditional projects--To be submitted when the Plan Year for requesting for CE funding is due.

APPROVAL PAGE
Final Project Proposal
Budget Year 2026-27

District: West Valley Mission Community College District

Project Location: Mission College
(College or Center)

Project: Student Campus Center Renovation

The district proposes funds for inclusion in the state capital outlay budget (check items):
preliminary plans ☒, working drawings ☒, construction ☒, equipment ☒

District Certification

Contact Person: Terrance DeGray **Telephone:** (804) 955-5512
(Vice Chancellor, Business & Fiscal Services)

E-Mail Address: Terrance.DeGray@wvm.edu **Fax:** _____

Approved for submission: _____ **Date:** _____
(Chancellor/President/Superintendent Signature)

District Board of Trustees Certification

The Governing Board of the District approves the submission of this application to the Board of Governors of the California Community Colleges and promises to fulfill the succeeding list of Project Terms and Conditions.

(President of the Board of Trustees Signature and Date)

(Secretary of the Board of Trustees Signature and Date)

Attach a copy of the Board Resolution that substantiates approval of the application and promises to fulfill the Project Terms and Conditions.

Submit proposal to:
Facilities Planning and Utilization
Chancellor's Office
California Community Colleges
1102 Q Street, 4th Floor (Ste. 6549)
Sacramento, CA 95811-6549

Chancellor's Office Certification

Reviewed by _____

Date Completed _____

PROJECT TERMS AND CONDITIONS

District: West Valley Mission Community College District **College/Center:** Mission College

Project: Student Campus Center Renovation

Budget Year: 2026-27

1. The applicant hereby requests state funds in the amount prescribed by law for the project named herein. All parts and exhibits contained in or referred to in this application are submitted with and made part of this application.
2. The applicant hereby assures the Board of Governors of the California Community Colleges that:
 - a. Pursuant to the provisions of Section 57001.5 of Title 5 no part of this application includes a request for funding the planning or construction of dormitories, stadia, the improvement of sites for student or staff parking, single-purpose auditoriums, or student centers other than cafeterias. The facilities included in the proposed project will be used for one or more of the purposes authorized in 57001.5 of Title 5.
 - b. Any state funds received pursuant to this application shall be used solely for defraying the development costs of the proposed project.

If the application is approved, the construction covered by the application shall be undertaken in an economical manner and will not be of elaborate or extravagant design or materials.
 - c. Pursuant to the provisions of Section 81837 of the *Education Code*, approval of the final plans and specifications for construction will be obtained from the Board of Governors of the California Community Colleges before any contract is let for the construction.
 - d. No changes in construction plans or specifications made after approval of final plans which would alter the scope of work, function assignable and/or gross areas, utilities, or safety of the facility will be made without prior approval of the Chancellor's Office of the California Community Colleges and the Department of General Services, Division of the State Architects.
 - e. Pursuant to the provisions of Section 57011 of Title 5, upon completion of a project the governing board shall submit to the Chancellor's Office, within 30 days after the closure of the current fiscal year, a final report on all expenditures in connection with the sources of the funds expended. The district shall be subject to a state post-audit review of fund claims for all such projects.
 - f. Architectural or engineering supervision and inspection will be provided at the construction site to ensure that the work was completed in compliance with the provisions of Section 81130 of the *Education Code* and that it conforms to the approved plans and specifications.

- g. Pursuant to the provisions of Section 8 of the *Budget Act*, no contract will be awarded prior to the allocation of funds to the Board of Governors by the Public Works Board.
- 3. It is understood by the applicant that:
 - a. No claim against any funds awarded on this application shall be approved which is for work or materials not a part of the project presented in this application as it will be finally allocated by the Public Works Board.
 - b. The failure to abide by each of the assurances made herein entitles the Board of Governors of the California Community Colleges to withhold all or some portion of any funds awarded on this application.
 - c. Any fraudulent statement which materially affects any substantial portion of the project presented in this application, as it may be finally approved, entitles the Board of Governors of the California Community Colleges to terminate this application or payment of any funds awarded on the project presented in this application.
- 4. It is further understood that:
 - a. The appropriation which may be made for the project presented in this application does not make an absolute grant of that amount to the applicant.
 - b. The appropriation is made only to fund the project presented in this application, as it is finally approved, regardless of whether the actual cost is less than or equals the appropriation.
 - c. A reduction in the scope of the project or assignable areas shall result in a proportionate reduction in the funds available from the appropriation.

West Valley-Mission Community College District (490)

Mission College (492)

Project: Student Campus Center Renovation

Rm Type	Description	TOP Code	Department	ASF	Sec. ASF	Increase In Space
050	Inactive Area	6910	Bookstore	0	4,010	-4,010
220	Spec Class Lab	0700	Information Technology	0	580	-580
220	Spec Class Lab	0701	Information Technology, General	0	557	-557
310	Office	0099	General Assignment	0	4,215	-4,215
310	Office	0701	Information Technology, General	0	273	-273
310	Office	6400	Other Student Services	1,686	0	1,686
310	Office	6450	Student Personnel Administration	0	276	-276
310	Office	6499	Other Student Services	0	1,033	-1,033
310	Office	6770	Logistical Services	503	362	141
310	Office	6940	Food Services	132	135	-3
310	Office	6999	Other Ancillary Services	0	2,111	-2,111
315	Office Service	0701	Information Technology, General	0	143	-143
315	Office Service	6770	Logistical Services	366	495	-129
315	Office Service	6999	Other Ancillary Services	0	16	-16
410	Read/Study Room	6120	Library	0	46	-46
530	Audio/Visual, Radio, TV	6130	Media Services	0	25	-25
540	Clinic St Care	6310	Counseling Services	0	134	-134
615	Assembly Service	6999	Other Ancillary Services	0	327	-327
630	Food Facilities	6940	Food Services	5,613	5,246	367
635	Food Facilities Service	6940	Food Services	978	2,204	-1,226
650	Lounge	6400	Other Student Services	5,690	0	5,690
650	Lounge	6999	Other Ancillary Services	0	426	-426
655	Lounge Service	6999	Other Ancillary Services	499	0	499
660	Merchandise Facility	6910	Bookstore	1,919	0	1,919
665	Merchandise Facility Service	6910	Bookstore	161	0	161
670	Recreation	6960	Students and Co-curricular Activities	2,122	0	2,122
675	Recreation Service	6960	Students and Co-curricular Activities	210	0	210
680	Meeting Room	6400	Other Student Services	4,228	0	4,228
680	Meeting Room	6770	Logistical Services	258	0	258
680	Meeting Room	6999	Other Ancillary Services	0	2,335	-2,335
685	Meeting Room Service	6400	Other Student Services	115	0	115
685	Meeting Room Service	6999	Other Ancillary Services	0	120	-120
690	Locker Room	6770	Logistical Services	0	94	-94
690	Locker Room	6940	Food Services	0	51	-51
715	DP/Computer Service	6130	Media Services	146	0	146
715	DP/Computer Service	6770	Logistical Services	0	250	-250

TOTAL	-	-		24,626	25,464	-838
-------	---	---	--	--------	--------	------

DISTRICT West Valley-Mission Community College District			CAMPUS Mission College		
Project Name: Student Campus Center Renovation		Date Prepared: 5/22/2024		Estimate CCI: 9654	
Prepared By: BKHUSHAL		Estimate EPI: 5455		CFIS Ref. #:	
		Budget Ref. #:			
	Total Cost	State Funded	District Funded		
			Supportable	Non Supportable	
1. SITE ACQUISITION (CCI: 9654)	\$0	\$0	\$0	\$0	
2. PRELIMINARY PLANS (CCI: 9654)	\$1,490,443	\$655,442	\$655,442	\$179,559	
2 - A. Architectural Fees for Preliminary Plans	\$904,390			\$139,657	
2 - B. Project Management for Preliminary Plans	\$258,397			\$39,902	
2 - C. Division of the State Architect Plan Check Fee	\$0			\$0	
2 - D. Preliminary Test (Soils Test, Geotech Report, Hazardous Material, Etc.)	\$104,571			\$0	
2 - E. Other Costs (Special Consultants, Printing, Legal, Etc.)	\$223,085			\$0	
3. WORKING DRAWINGS (CCI: 9654)	\$1,387,227	\$588,883	\$588,883	\$209,461	
3 - A. Architectural Fees for Working Drawings	\$1,033,588			\$159,608	
3 - B. Project Management for Working Drawings	\$0			\$0	
3 - C. Division of the State Architect Plan Check Fee	\$203,126			\$38,452	
3 - D. Community Colleges Plan Check Fee	\$73,828			\$11,401	
3 - E. Other Costs (Special Consultants, Printing, Legal, Etc.)	\$76,685			\$0	
(Total PW may not exceed 13% of construction)	\$0			\$0	
4. CONSTRUCTION - HARD COSTS (CCI: 9654)	\$25,839,701	\$11,427,388	\$10,422,108	\$3,990,205	
4 - A. Utility Service	\$749,007			\$0	
4 - B. Site Development - Service	\$0			\$0	
4 - C. Site Development - General	\$2,517,549			\$0	
4 - D. Site Development - Other	\$5,124,730			\$0	
4 - E. Reconstruction	\$13,066,223			\$0	
4 - F. New Construction (Building) (w/Group 1 equip)	\$0			\$0	
4 - G. Board of Governor's Energy Policy Allowance (2% or 3%)	\$391,987			\$0	
4 - H. Other	\$3,990,205			\$3,990,205	
5. CONTINGENCY (CCI: 9654)	\$1,808,779	\$764,732	\$764,732	\$279,314	
5. Contingency	\$1,808,779			\$279,314	
6. ARCHITECTURAL AND ENGINEERING OVERSIGHT (CCI: 9654)	\$645,993	\$273,119	\$273,119	\$99,755	
6. Architectural and Engineering Oversight	\$645,993			\$99,755	
7. TESTS AND INSPECTIONS (CCI: 9654)	\$612,097	\$258,788	\$258,788	\$94,521	
A. Tests	\$258,397			\$0	
B. DSA Inspections	\$353,700			\$0	
8. CONSTRUCTION MANAGEMENT (CCI: 9654)	\$516,794	\$218,495	\$218,495	\$79,804	
8. Construction Management	\$516,794			\$79,804	
9. TOTAL CONSTRUCTION (Items 4 through 8) (CCI: 9654)	\$29,423,363	\$12,942,522	\$11,937,242	\$4,543,600	
Total Construction Costs	\$29,423,363			\$4,543,600	
10. FURNITURE AND GROUP II EQUIPMENT (EPI: 5455)	\$1,005,281	\$0	\$1,005,281	\$0	
10 - A. Furniture and Group II Equipment	\$1,005,281			\$0	
11. Total Project Costs (Items 1, 2, 3, 9, and 10)	\$33,306,314	\$14,186,847	\$14,186,848	\$4,932,619	
12. Project Data	Gross Square Feet	Assignable Square Feet	ASF:GSF Ratio	Unit Cost Per ASF	Unit Cost Per GSF
New Construction	0	0	0%	\$0.00	\$0.00
Reconstruction	39,421	24,626	62%	\$530.59	\$331.45
13. Anticipated Time Schedule					
Start Preliminary Plans	7/1/2026	Advertise Bid for Construction		7/15/2028	
Start Working Drawings	3/1/2027	Award Construction Contract		11/1/2028	
Complete Working Drawings	10/1/2027	Advertise Bid for Equipment		10/1/2029	
DSA Final Approval	6/1/2028	Complete Project and Notice of Completion		4/1/2030	
14.	State Funded	District Funded		District Funded Total	
		Supportable	Non Supportable		
Preliminary Plans	\$655,442	\$655,442	\$179,559	\$835,001	
Working Drawings	\$588,883	\$588,883	\$209,461	\$798,344	
Construction	\$12,942,522	\$11,937,242	\$4,543,600	\$16,480,842	
Equipment	\$0	\$1,005,281	\$0	\$1,005,281	
Total Costs	\$14,186,847	\$14,186,848	\$4,932,619	\$19,119,467	
% of SS Costs	42.60%	57.40%	Project Total	\$33,306,314	
Points % Calc	49.30%	50.70%	SS Total	\$28,373,695	

Report Generated: 5/22/2024

QUANTITIES AND UNIT COSTS SUPPORTING THE JCAF32

1	Site Acquisition				
2	Plans				\$1,490,443
	A. Architect's Fee (Preliminary Plans)				
	RECONSTRUCTION x 10% x 35%				\$904,390
	B. Project Management Fee (Preliminary Plans)				
	CONST x 1%				\$258,397
	C. Division of the State Architect Plan Check Fee				\$0
	All allocated to Working Drawings Phase				
	D. Preliminary Tests (soils, hazardous materials)				
	Soil Testing				\$48,800
	Geotechnical Testing				\$55,771
	E. Other Costs				
	Design Management/Constructability Consultant				\$48,800
	Design Consultant				\$76,685
	Data/Technology Consultant				\$62,743
	CEQA Consultant				\$34,857
3	Working Drawings				\$1,387,227
	A. Architect's Fee (Working Drawings)				
	RECONSTRUCTION x 10% x 40%				\$1,033,588
	B. Project Management Fee (Working Drawings)				
	All Allocated to Preliminary Plans				\$0
	C. Office of the State Architect, Plan Check Fee				
	Plan Check Fee, Structural, Fire, Life Safety Review				\$203,126
	D. Community College Plan Check Fee				
	CONST x 0.0028571				\$73,828
	E. Other Costs:				
	Legal Services				\$41,828
	Printing Fees				\$20,914
	Advertising				\$13,943
4	Construction				\$25,839,701
		Quantity	Unit	Cost per Unit	Total Cost
	A. Utility Services				
	Fire Water modifications, allowance	1	LS	\$83,642.70	\$83,643
	Domestic Water, modifications as needed	1	LS	\$63,962.07	\$63,962

QUANTITIES AND UNIT COSTS SUPPORTING THE JCAF32

	Sanitary Sewer, modifications as needed	1	LS	\$162,365.24	\$162,365
	Sanitary Sewer, new	1	LS	\$117,141.96	\$117,142
	Storm Drain, modifications as needed	1	LS	\$127,432.12	\$127,432
	Storm Drain, new	1	LS	\$93,717.31	\$93,717
	Replace existing grease interceptor, allow 2000 gallons	1	LS	\$100,745.71	\$100,746
	<i>Subtotal Utility Services</i>				<i>\$749,007</i>
	B. Site Development Service				
	<i>Not Applicable</i>				
	<i>Subtotal Site Development Service</i>				<i>\$0</i>
	C. Site Development General				
	AC Paving, Patching/Repairs Near Loading Docks	1	LS	\$51,544.52	\$51,545
	Standard Concrete Paving, 90% of Site	1	LS	\$1,268,557.55	\$1,268,558
	Sawcut	1	LS	\$23,429.23	\$23,429
	Demo Existing Concrete	1	LS	\$158,569.69	\$158,570
	Rough and Fine Grading at New Concrete Paving/Sidewalks	1	LS	\$237,854.54	\$237,855
	Concrete Curbs	1	LS	\$140,575.97	\$140,576
	Concrete Seat Walls	1	LS	\$468,586.56	\$468,587
	Landscape and Irrigation, 10% of site	1	LS	\$70,519.47	\$70,519
	Site Specialties (Benches, signage, trash receptacles, etc.)	1	LS	\$97,911.16	\$97,911
	<i>Subtotal Site Development General</i>				<i>\$2,517,549</i>
	D. Other Site Development				
	Mandatory Seismic Upgrades	39,421	GSF	\$130.00	\$5,124,730
	<i>Subtotal Other Site Development</i>				<i>\$5,124,730</i>
	E. Reconstruction				
	<i>Based on CCI 9654 (75% of New Construction):</i>				
	310 Office (6400 Other Student Services)	1,686	ASF	\$809.00	\$1,022,981
	310 Office (6770 Logistical Services)	503	ASF	\$809.00	\$305,195
	310 Office (6940 Food Services)	132	ASF	\$809.00	\$80,091
	315 Office Service (6770 Logistical Services)	366	ASF	\$809.00	\$222,071
	630 Food Facilities (6940 Food Services)	5,613	ASF	\$662.00	\$2,786,855
	635 Food Facilities Service (6940 Food Services)	978	ASF	\$662.00	\$485,577
	650 Lounge (6400 Other Student Services)	5,690	ASF	\$795.00	\$3,392,663
	655 Lounge Services (6400 Other Student Services)	499	ASF	\$795.00	\$297,529
	660 Merchandise Facility (6910 Bookstore)	1,919	ASF	\$0.00	\$0
	665 Merchandise Facility Service (6910 Bookstore)	161	ASF	\$0.00	\$0
	670 Recreation (6960 Students and Co-curricular Activities)	2,122	ASF	\$937.00	\$1,491,236
	675 Recreation Service (6960 Students and Co-curricular Activities)	210	ASF	\$937.00	\$147,578
	680 Meeting Room (6400 Other Student Services)	4,228	ASF	\$795.00	\$2,520,945

QUANTITIES AND UNIT COSTS SUPPORTING THE JCAF32

	680 Meeting Room (6770 Logistical Services)	258	ASF	\$795.00	\$153,833
	685 Meeting Room Service (6400 Other Student Services)	115	ASF	\$795.00	\$68,569
	715 DP/Computer Service (6130 Media Services)	146	ASF	\$832.00	\$91,104
	<i>Subtotal Reconstruction</i>				<i>\$13,066,223</i>
	F. New Construction				
	<i>Not Applicable</i>				
	<i>Subtotal New Construction</i>				<i>\$0</i>
	G. Other Construction				
	BOG Energy incentive allowance (3% of Reconstruction)				\$391,987
	<i>Subtotal BOG Allowance</i>				<i>\$391,987</i>
	H. Other				
	Non-State Supportable Cost Exceeding CCI 9654 Guideline	24,626	ASF	\$106.12	\$2,613,245
	Non-State Supportable Costs: 660-665 Merchandise Facility	2,080	ASF	\$662.00	\$1,376,960
	<i>Subtotal Other Construction</i>				<i>\$3,990,205</i>
5	Contingency				\$1,808,779
	RECONSTRUCTION x 7%				\$1,808,779
6	Architectural & Engineering & Oversight				\$645,993
	RECONSTRUCTION x 10% x 25%				\$645,993
7	Tests & Inspections				\$612,097
	(a) Test = 1% x CONST				\$258,397
	(b) Inspection = 18 months * \$19,650				\$353,700
8	Construction Management				\$516,794
	(a) Construction Management CONST x 2%				\$516,794
9	Total Construction Costs				\$29,423,363
	(Items 4 through 8 above)				
10	Furniture & Group II Equipment				\$1,005,281
11	Total Project Cost				\$33,306,314
	(Items 1, 2, 3, 9 and 10)				
12	Cost per Gross Square Foot	39,421	GSF		\$331

BOARD OF GOVERNORS ENERGY AND SUSTAINABILITY POLICY

This project will be designed to exceed Title 24, Part 6 Energy Code by at least 15%, consistent with the Board of Governors Energy and Sustainability policy. The design should incorporate sustainable goals for site and energy efficiency, water use reduction, storm water management, occupant health as well as minimizing the buildings impact on the environment both by design and construction. Strategies will consider:

- Natural and native planting materials will be incorporated around the building to minimize, if not eliminate, the irrigation demand.
- Concrete walkways will be minimized to reduce stormwater runoff and promote natural filtration into the soil as well as a reduction in the heat island effect.
- Solar heat gain reduction measures will be used. Overhangs will be incorporated to shade glazing. Low E glazing will be incorporated to reduce heat gain. Roofing will incorporate cool roofing to reduce the heat island effect and heat gain.
- Heating and cooling will be provided by a highly energy efficient HVAC system with controls designed to maximize efficiency.
- Natural lighting will be incorporated into most spaces.
- Energy saving lighting will include automatic lighting controls and sensors.
- Interior materials will be low in volatile organic compounds, high in recycled content.
- Water efficient fixtures, faucets and devices will be incorporated.
- A strict recycling program will be required during construction.
- Requested participation in the local utility's energy incentive program.
- Photovoltaic panels will be incorporated where appropriate.
- Durable systems and finish with long life cycles that minimize maintenance and replacement.
- Optimization of indoor environmental quality for occupants with high efficiency industrial ventilation.
- Utilization of environmentally preferable products and processes, such as recycled content materials and recyclable materials.
- Procedures that monitor, trend and report operational performance as compared to the optimal design and operating parameters to the campus' central energy management system.
- Space will be provided throughout the building to support an active recycling program.

DEPARTMENT: _____

PROJECT TITLE: _____

TOTAL REQUEST (DOLLARS IN THOUSANDS): \$ _____ MAJOR/MINOR: _____

PHASE(S) TO BE FUNDED: _____ PROJ CAT: _____ CCCI/EPI: _____

SUMMARY OF PROPOSAL:

******* THIS PAGE IS TO BE COMPLETED BY FPU. *******

HAS A BUDGET PACKAGE BEEN COMPLETED FOR THIS PROJECT? (E/U/N/?): _____

REQUIRES LEGISLATION (Y/N): _____ IF YES, LIST CODE SECTIONS: _____

REQUIRES PROVISIONAL LANGUAGE (Y/N) _____

IMPACT ON SUPPORT BUDGET: ONE-TIME COSTS (Y/N): _____ FUTURE COSTS (Y/N): _____

FUTURE SAVINGS (Y/N): _____ REVENUE (Y/N): _____

DOES THE PROPOSAL AFFECT ANOTHER DEPARTMENT (Y/N): _____ IF YES, ATTACH
COMMENTS OF AFFECTED DEPARTMENT SIGNED BY ITS DIRECTOR OR DESIGNEE.

SIGNATURE APPROVALS:

PREPARED BY DATE REVIEWED BY DATE

DEPARTMENT DIRECTOR DATE AGENCY SECRETARY DATE

DOF ANALYST USE

DOF ISSUE # _____ PROGRAM CAT: _____ PROJECT CAT: _____ BUDG PACK STATUS: _____

ADDED REVIEW: SUPPORT: _____ OCIU: _____ FSCU/ITCU: _____ OSAE: _____ CALSTARS: _____

PPBA: _____

Date: _____

DF-151 (Rev. 04/11)

RESPONSES TO SPECIFIC REQUIREMENTS OF THE STATE ADMINISTRATIVE MANUAL

A. PURPOSE OF THE PROJECT:

A1. EXECUTIVE SUMMARY

Mission College's Campus Center building was constructed in 1999 and has had no major renovations since its original construction. The proposed project will renovate the existing Campus Center, which encompasses 39,421 of Gross Square Feet (GSF) and 24,626 of Assignable Square Feet (ASF). The existing Campus Center houses the campus cafeteria/dining facilities, bookstore, meeting rooms, student services offices, and campus parking/police functions. Renovation of the building will upgrade infrastructure systems, provide for a more comprehensive approach to student life, and improve safety/security and dining services. Scope of work will include, but not limited to, the replacement of the following systems: roof, HVAC, plumbing, data/ telecommunication, and electrical. The project will also include (ADA) accessibility improvements, mandatory seismic rehabilitation, and interior reconfiguration and repurposing.

Functional space within the renovated building will include 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space.

Total project cost is estimated to be \$33,306,314 (per Construction Cost Index (CCI) 9654) and is not escalated to the mid-point of construction.

The State Capital Outlay system considers the proposed project as a Category M project, modernization of institutional support space.

A2. PROBLEM STATEMENT

Mission College was established in 1979 in Santa Clara, California. The College is one of two colleges in the West Valley - Mission Community College District, which serves the cities of Campbell, Los Gatos, Morgan Hill, Monte Sereno, Santa Clara, and San Jose. West Valley Mission Community College District is not located in an area of high need as identified in the Vision for Success. According to the California Community Colleges Chancellor's Office (CCCCO) Datamart, approximately 3,363 (30%) students at Mission College received some sort of financial aid during the 2022-2023 academic year. Approximately 2,867 students received California College Promise Grants, 1,219 received Pell Grants, and 412 received Supplemental Educational Opportunity Grants.

During the Fall 2022 term, Mission College employed approximately 324 Full-Time Equivalent (FTE) employees campuswide. During the 2022-2023 academic year, the College enrolled approximately 4,789 Full-Time Equivalent Students (FTES) in over 70 different degree and certificate programs.

Infrastructure Deficiencies/Safety Issues:

Users within the existing Campus Center face challenges caused by deficiencies of building systems and infrastructure. The existing facility faces ongoing and disruptive electrical issues that hinder the ability of the College to effectively deliver essential programs and services to the student body. While many mitigation attempts have been made to rectify issues caused by deficient building systems, they have been only marginally effective in solving the problems faced by the building's users and have not resulted in a permanent, long-term solution to the issues presented. Specifically:

- Power to the entire building often shuts down as the result of several persistent electrical shorts in the system that trip the main breaker.
- The existing lighting system has been identified as the cause of the shorts, however, since 2015, lighting consultants as well as the lighting controls manufacturer itself have not been able to provide a long-term remedy for the electrical issues within the building.
- Natural corrosion of copper piping within the building has caused leaks to the roof and the plumbing underneath dining spaces. Plumbing leaks have also disrupted the hot water distribution system within the building and create challenges for proper food preparation. The Mission College cafeteria/dining function is completely operated by students and staff within its Hospitality Department. Thus, these building systems deficiencies directly disrupt instructional activities.
- Security systems within the existing structure currently do not meet the standards set forth by the West Valley - Mission Community College District. Stiles at the bookstore and dining areas are slim line and do not allow for installation of District recommended security systems.

Programmatic Issues:

The Mission College Campus Center houses the following programs, services, and functions: cafeteria/dining facilities, bookstore, meeting rooms, computer labs, faculty offices, student services offices, the campus safety/security functions. The existing structure is not suited to meet existing and anticipated student demand for these services. Credit loads of students were steadily increasing in recent years before the COVID-19 pandemic.

As students return to campus and enrollment recovers over the next few years, it is anticipated that the average student will require more access to institutional support services/space than they have in the past. Thus, programs and services in the Campus Center are facing larger demand than the existing building supports. The existing Campus Center is not configured in a way to maximize access to student services. DSPS and Veteran's services are currently located on the second floor of the Campus Center. Students with disabilities need to use stairs or elevators to access DSPS services, creating an additional barrier for students who are limited with mobility, especially during peak foot traffic times on campus.

The wireless internet network within the existing Campus Center cannot support student use in a variety of ways. The Wi-Fi network currently does not have enough bandwidth to support the technological needs of students and staff during times of high on-campus traffic. Students and

staff experience slow internet speeds and frequent disconnections from their devices. Additionally, computer server rooms need to be upgraded in order to accommodate the technological needs of the programs within the existing facility. As the need for reliable and adequate access to the Internet on campus grows, server rooms in the building will require more space and additional cooling capacity than what the existing building currently provides.

Several steps have been taken to mitigate the negative effects of the aforementioned deficiencies within the Campus Center. HVAC units, compressors, and controls in the building have been replaced. The plumbing systems on the first floor, second floor, and beneath the dining services areas has been patched and replaced where possible. LED lighting has been installed in the dining areas. The building electrical systems have also been switch-tested and recalibrated for sensitivity. While many mitigation attempts have been made to rectify issues caused by deficient building systems, they have been only marginally effective in solving the problems faced by the building's users and have not resulted in a permanent, long-term solution to the issues presented.

A3. SOLUTION CRITERIA

An effective solution to current problems experienced by the Campus Center would address the following goals:

- Educational Impact—Repurpose existing space to better respond to space needs for institutional support services
- Educational Impact – Reconfigure functional adjacencies for an effective flow of communication, collaboration, and resource allocation.
- Campus Integration – Consistency with goals/objectives within the College's Educational and Facilities Master Plans
- Safety/Security – Improve fire/life safety systems, accessibility, and building code compliance
- Energy Efficiency and Sustainability – Improve water and energy efficiency
- Delivery Timeline – Deliver a solution in the shortest amount of time.
- Cost – Is the least cost solution

B. RELATIONSHIP TO THE STRATEGIC PLAN:

Mission College's Student Campus Center Renovation project seeks to advance the goals of the state-wide Vision 2030 Plan, an effort to promote equity in success, access, and support. The College's own Educational and Facilities Master Plan (EFMP) student success goals align with the state-wide Vision 2030 Plan. The EFMP states that facility projects on campus should promote academic success and create dynamic, innovative student services programs that address the richness of Mission College's student population and community.

The proposed project solution should not only upgrade space on campus that is necessary for student collaboration and study, but also enhance the ability of the College to deliver essential services critical to fostering student success and access. The solution must also seek to meet the State's environmental sustainability goals via integration of modern and eco-friendly architectural design practices.

C. ALTERNATIVES:

This section analyzes four alternatives as potential viable solutions to the problems discussed in the above Problem Statement. The Solution Criteria Matrix identifies how these alternatives respond to each measure set forth in the Solution Criteria section. The Economic Matrix at the end of this section details the fiscal impact of each alternative.

- Alternative #1 – Student Campus Center Renovation
- Alternative #2 – Student Campus Center Replacement
- Alternative #3 – Installation of Portables/Modulars
- Alternative #4 – Lease Space Off-Campus

Alternative #1 – Campus Center Renovation

Reconstructs existing Campus Center to 24,626 ASF (39,421 GSF). Functional space within the building will include 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space. The estimated cost of this alternative at Construction Cost Index (CCI) 9654 and Equipment Price Index (EPI) 5455 is \$33,306,314 (not escalated to mid-point of construction).

Pros:

- Educational Impact—Repurposes existing space to better respond to space needs for institutional support services
- Educational Impact – Reconfigures functional adjacencies for an effective flow of communication, collaboration, and resource allocation.
- Campus Integration – Is consistent with goals/objectives within the College’s Educational and Facilities Master Plans
- Safety/Security – Improves fire/life safety systems, accessibility, and building code compliance
- Energy Efficiency and Sustainability – Improves water and energy efficiency
- Delivery Timeline – Delivers a solution in the shortest amount of time.
- Cost – Is the least cost solution

Cons:

- None

Alternative #2 – Campus Center Replacement

Constructs a new Campus Center of 24,626 ASF (39,421 GSF) to replace the existing Campus Center. Functional space within the building will include 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space. As a secondary effect of this alternative, the existing Campus Center would be demolished. The estimated cost of this alternative at Construction Cost Index (CCI) 9654 and Equipment Price Index (EPI) 5455 is \$47,502,361 (not escalated to mid-point of construction).

Pros:

- Educational Impact—Repurposes existing space to better respond to space needs for institutional support services

- Educational Impact – Reconfigures functional adjacencies for an effective flow of communication, collaboration, and resource allocation.
- Campus Integration – Is consistent with goals/objectives within the College’s Educational and Facilities Master Plans
- Safety/Security – Improves fire/life safety systems, accessibility, and building code compliance
- Energy Efficiency and Sustainability – Improves water and energy efficiency

Cons:

- Delivery Timeline – Does not deliver a solution in the shortest amount of time
- Cost – Is not the least cost solution.

Alternative #3 – Installation of Portables/Modulars

Installs 24,626 ASF (39,421 GSF) of portable/modular buildings. Functional space will include 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space. Portables would require replacement every 30 years to maintain building standards and would require at least 2 installations to compare this option to a permanent structure. As a secondary effect of this alternative, the existing Campus Center would be demolished. The estimated cost of this alternative at Construction Cost Index (CCI) 9654 and Equipment Price Index (EPI) 5455 is \$62,630,108 (not escalated to mid-point of construction).

Pros:

- Educational Impact—Repurposes existing space to better respond to space needs for institutional support services
- Safety/Security – Improves fire/life safety systems, accessibility, and building code compliance

Cons:

- Educational Impacts – Does not reconfigure functional adjacencies for an effective flow of communication, collaboration, and resource allocation (portables would require a large footprint which may not improve overall space configuration and adjacencies)
- Campus Integration – Is not consistent with goals/objectives within the College’s Educational and Facilities Master Plans (does not provide a permanent long-term solution, increases dependency on temporary facilities)
- Energy Efficiency and Sustainability – Does not improve water and energy efficiency (large footprint and requires duplication of building systems)
- Delivery Timeline – Does not deliver a solution in the shortest amount of time (multiple installation phases impact project duration)
- Cost – Is not the least cost solution (multiple installation phases impact project cost)

Alternative #4 - Leasing an Off-Campus Facility

Lease a 24,626 ASF (39,421 GSF) facility off-campus. The leased building will 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space. To compare this alternative to a facility that is owned by the District, the lease would have to be maintained for approximately 60 years. As a secondary effect of this alternative, the existing Campus Center would be demolished. The estimated cost of this

alternative at CCI 9654 and EPI 5455 is \$123,336,528 (not including costs for tenant improvements).

Pros:

- Safety/Security – Improves fire/life safety systems, accessibility, and building code compliance
- Energy Efficiency and Sustainability – Improves water and energy efficiency

Cons:

- Educational Impact – Does not repurpose existing space to better respond to space needs for institutional support services (disjoins students/faculty from the main campus)
- Educational Impact – Does not reconfigure functional adjacencies for an effective flow of communication, collaboration, and resource allocation (disjoins students/faculty from the main campus)
- Campus Integration – Is not consistent with goals/objectives within the College's Educational and Facilities Master Plans (disjoins students/faculty from the main campus and the College may not be able to fully control hours of operation/scheduling)
- Delivery Timeline – Does not deliver a solution in the shortest amount of time (requires long-term lease agreement and substantial tenant improvements)
- Cost – Is not the least cost solution (requires long-term lease agreement, substantial tenant improvements, and strains campus operational budget)

SOLUTION CRITERIA MATRIX

SOLUTION CRITERIA	ALTERNATIVES			
	#1 Reconstruction	#2 Replacement	#3 Temporary Portables	#4 Lease Space Off-Campus
Repurpose space to better respond to needs of institutional support services	YES	YES	YES	NO
Reconfigure adjacencies for an effective flow of communication, collaboration, and resource allocation	YES	YES	NO	NO
Consistency with goals/objectives within the College's Educational and Facilities Master plans	YES	YES	NO	NO
Improve fire/life safety systems, accessibility, and building code compliance	YES	YES	YES	YES
Improve water and energy efficiency	YES	YES	NO	YES
Deliver a solution in the shortest amount of time	YES	NO	NO	NO
Is the least cost solution	YES	NO	NO	NO

ECONOMIC ANALYSIS

ECONOMIC ANALYSIS	(All Costs estimated to CCI 9654, EPI 5455)			
	#1	#2	#3	#4
	Reconstruction	New Construction	Temporary Portables	Lease Space Off-Campus
Site Acquisition	\$0	\$0	\$0	\$0
Plans and Working Drawings	\$2,877,669	\$3,517,260	\$8,397,246	Unknown
Construction Costs:				
Utility Service	\$749,007	\$1,450,877	\$1,498,014	Unknown
Site Development-Service	\$0	\$2,176,316	\$4,352,632	Unknown
Site Development-General	\$2,517,549	\$3,627,193	\$5,035,097	Unknown
Other Site	\$5,124,730	\$0	\$0	Unknown
Reconstruction	\$13,066,223	\$0	\$0	Unknown
New Construction	\$0	\$24,181,288	\$0	Unknown
Other Construction	\$4,382,191	\$1,429,730	\$714,309	Unknown
Construction Soft Costs	\$3,583,663	\$4,228,802	\$5,912,103	Unknown
Total Construction Costs	\$29,423,363	\$37,094,206	\$17,512,155	Unknown
Equipment (Group II)	\$1,005,281	\$1,005,281	\$1,005,281	\$1,005,281
Other – Lease Space or Portable Costs	\$0	\$5,885,614	\$35,715,426	\$122,331,247
Total Project Cost @ CCI 9654 and EPI 5455	\$33,306,314	\$47,502,361	\$62,630,108	\$123,336,528
Escalated per Department of Finance Budget Letter BL05-21	<u>CCC Calculates this amount based on latest DOF directions</u>			

- 1.) Professional estimate obtained from Cummings & ALMA Strategies at CCI 9654 and EPI 5455.
- 2.) This estimate includes replacement of the Campus Center (24,626 ASF/39,421 GSF). The estimate is based on CCI 9654 and EPI 5455.
- 3.) Portables are estimated to cost \$453 per square foot (39,421 GSF x \$453 = \$17,857,713). Total cost estimate includes replacement for every 30 years over 60-year period \$17,857,713 x 2 installations = \$35,715,426). Project costs for preliminary planning, working drawings, soft construction, and equipment were estimated using State allowances on a JCAF 32 form at CCI 9654 and EPI 5455.
- 4.) Lease rates are approximately \$51.72 annually per sq. ft. x 39,421 GSF x 60 years = \$123,336,528 (\$51.72 annual per sq. foot lease cost was obtained using Q1 2024 market estimates from Cushman and Wakefield for the City of Santa Clara and does not include tenant improvement costs).

D. RECOMMENDED SOLUTION:

D1. WHICH ALTERNATIVE AND WHY?

The recommended solution is **Alternative #1**, to renovate the existing Campus Center. This option will meet each of the solution criteria by repurposing existing space to better respond to campus needs, upgrading building systems/infrastructure, and reconfiguring existing space for efficiency. The recommended option will comply with ADA standards and is consistent with the College's Educational Master Plan. In addition, Alternative #1 is also the least cost solution and will address each of the solution criteria in the shortest possible time.

Alternative #2, replacing the existing Campus Center with a new building, meets most of the identified solution criteria, however, will take more time and money to complete than the recommended solution. Alternative #3 requires the installation of portables, which conflicts with the College's Education and Facilities Master Plans goals to reduce the use of temporary structures on campus. Installation of portables would require a large footprint and require the College to use sites that are needed for other capital construction projects or programs. Alternative #3 is the second-most costly solution and will not reconfigure space in an efficient manner.

Leasing of space off-campus (Alternative #4) does not provide a viable solution for the future of student Campus Center services at the College. A lease would need to be maintained for at least 60 years to compare this option to a permanent facility that is owned by the District. Significant tenant improvements would likely be required to support the space needs of the campus. This option will also place a heavy strain on the operational budget of the College. Housing essential services/programs such as campus police and food services off-campus will reduce their access to the main campus and create logistical challenges in efficiently and effectively functioning.

D2. DETAILED SCOPE DESCRIPTION

The Student Campus Center Renovation project would renovate the existing Campus Center at Mission College. The proposed project will encompass 2,687 ASF of Office, 6,591 ASF of Food Service, 6,189 ASF of Lounge, 2,080 ASF of Bookstore, and 7,079 ASF of Other support space. Programs and services that will benefit from the reconfiguration of space include Associated Student Organizations, Student Activities/Clubs, Learning Resources, Food Services, and Campus Police. The renovation will also provide an upgraded student club, study, multicultural center, and collaboration space for students.

During construction, some users within the existing building may need to be relocated into temporary housing until the project is ready for occupancy. Costs associated with relocation and swing space are not included in the proposed project scope.

Building design will include features to exceed the requirements of Title 24, part 6 Energy Efficiency by at least 15%. On-campus water usage will also be made more efficient as a result of the proposed project. The project will include the installation of increasingly efficient mechanical and electrical devices, as well as the use of improved materials, to ultimately reduce

operational and maintenance costs. The building will be reconstructed to current code and accessibility (ADA) requirements. The identification and removal of any hazardous materials used during construction of the original building is included within the project scope.

The proposed project is aimed at providing Mission College with a renovated Student Campus Center that would positively impact student services programs while taking into account the College's capacity-load ratios. The proposed project will decrease laboratory space on campus by 1,137 ASF and contribute towards decreasing lab capacity-load from 239% at project start to 230% by occupancy. The project will also decrease overall office space on campus by 6,372 ASF and reduce office capacity-load from 86% at project start to 78% by occupancy. The project will decrease library space on campus by 46 ASF, and the library capacity-load is expected to decrease from 122% to 121% by occupancy. Most space within the proposed project (21,939 ASF) is attributable to non-capacity load bearing room use types.

The table below outlines the net effect of this project on campus ASF and capacity load ratios:

Space Analysis

Type	Lecture	Lab	Office	Library	AV/TV	Other	Total
Primary ASF	0	0	2,687	0	0	21,939	24,626
Secondary ASF	0	-1,137	-9,059	-46	-25	-15,197	-25,464
Net ASF	0	-1,137	-6,372	-46	-25	6,742	-838
Initial Cap/Load (FY2026)	264%	239%	86%	122%	35%	N/A	149%
Final Cap/Load (FY2029-)	260%	230%	78%	121%	35%	N/A	144%

The proposed reconstruction does not adversely impact the campus operations budget and is the least cost solution. Total project costs are estimated at \$33,306,314 based on CCI 9654 and EPI 5455 (excluding factors for escalation to mid-point of construction). The total project cost breakdown by phase is \$1,490,443 for preliminary planning, \$1,387,227 for working drawings, \$29,423,363 for total construction, and \$1,005,281 for group II equipment. The District is committed to contributing 50 percent of total State-supportable project costs. The District will also fund 100 percent of all non-state supportable costs associated with renovation of bookstore space within the building and non-State supportable costs exceeding guidelines for hard construction. (For additional information on non-State supportable costs costs, see "Justification for Costs Exceeding State Guidelines" section.)

D3. BASIS FOR COST INFORMATION

Cost information for the project was provided by the professional firms of Cummings and ALMA Strategies and reflects their experience of similar projects in the general area. Soft costs associated with the project are based on state supportable cost allowances recommended within the State's JCAF 32 Form (CCCI 9654 and EPI 5455) and have not been escalated to the mid-point of construction. West Valley - Mission Community College District has pledged to fund 50% of State supportable costs and all Non-State supportable costs with local funds. Additionally, an explanation for hard construction costs exceeding state guidelines is provided in the "Justification for Costs Exceeding State Guidelines" section of this document.

D4. FACTORS/BENEFITS FOR RECOMMENDED SOLUTION OTHER THAN THE LEAST EXPENSIVE ALTERNATIVE

Aside from doing nothing, the recommended option presents the least cost alternative and is the only feasible option that provides an adequate solution to each of the identified solution criteria.

D5. COMPLETE DESCRIPTION OF IMPACT ON SUPPORT BUDGET

Mission College affirms that it will budget for ongoing maintenance and operations costs associated with the proposed project using local resources. This project will not result in a need for additional faculty or staff positions. Any additional expenses for faculty/staff to support expanding or growing programs will come from increased apportionments generated by such programs. This project will include the installation of increasingly efficient building systems and materials that will ultimately reduce maintenance and operations costs. The replacement of aging infrastructure and building systems will contribute to decreasing expenses which are currently endured by the operating budget. For further analysis, refer to the “Analysis of Future Cost” in section 9.1 of this document.

D6. IDENTIFY AND EXPLAIN ANY PROJECT RISKS

There are no unusual or extraordinary project risks. Any removal of hazardous materials during reconstruction will be conducted by persons trained for such work. Other portions of the work will be executed by people who are familiar with construction, its attendant risks, and who will implement activities as necessary to minimize risks.

D7. LIST REQUESTED INTERDEPARTMENTAL COORDINATION AND/OR SPECIAL PROJECT APPROVAL

- The Division of State Architect – Title 24 structural, access compliance and energy reviews
- State Fire Marshal – Fire/life safety
- State Public Works Board and Department of Finance – Approval of Preliminary Plans and Working Drawings

E. CONSISTENCY WITH GOVERNMENT CODE SECTION 65041.1

The California Community Colleges are exempt from these specific provisions of this legislation.

F. ATTACHMENTS:

JCAF 31

JCAF 32

JCAF 33

CALIFORNIA ENVIRONMENTAL QUALITY ACT
(Reference: California Code of Regulations, Title 5 Section 57121)

District will have CEQA review requirements completed prior to request for Preliminary Plans approval.

ANALYSIS OF FUTURE COSTS

Provide an economic analysis of additional instructional, administrative, and maintenance costs resulting from the proposed project, including personnel years. Disclose all new courses or programs to be housed in the project that may need Chancellor's Office review.

Personnel Costs

Certificated:

No additional certificated staff need estimated with the proposed new facility

Classified:

No additional classified staff need estimated with the proposed new facility.

Depreciation, Maintenance, and Operation

The energy efficient building systems, equipment and technology throughout the renovated building will decrease maintenance and operations costs from current levels. The project will not result in an increase to the overall campus assignable square footage. Energy efficiency measures will help reduce energy cost per square foot over the current building, but custodial costs and ongoing maintenance will be relatively unchanged.

Program/Course/Service Approvals

List all new programs/courses/services to be housed in this project or its secondary effects and give the date of approval. If there are no new programs/courses/services for which approval is required, please so state. This is not required for equipment-only projects.



Name of New Program/Course/Service

Date of Approval

None

DIAGRAMS OF CAMPUS, PROJECT SITE, BUILDING AREAS, AND ELEVATIONS


Provide the following pre-schematics in lieu of this sheet: Campus Plot Plan, Site Plan, Floor Plans, and Exterior Elevations. If the project has unusual characteristics that require further explanation, please provide the following conceptual drawings as needed: Electrical Plans and Mechanical Plans.

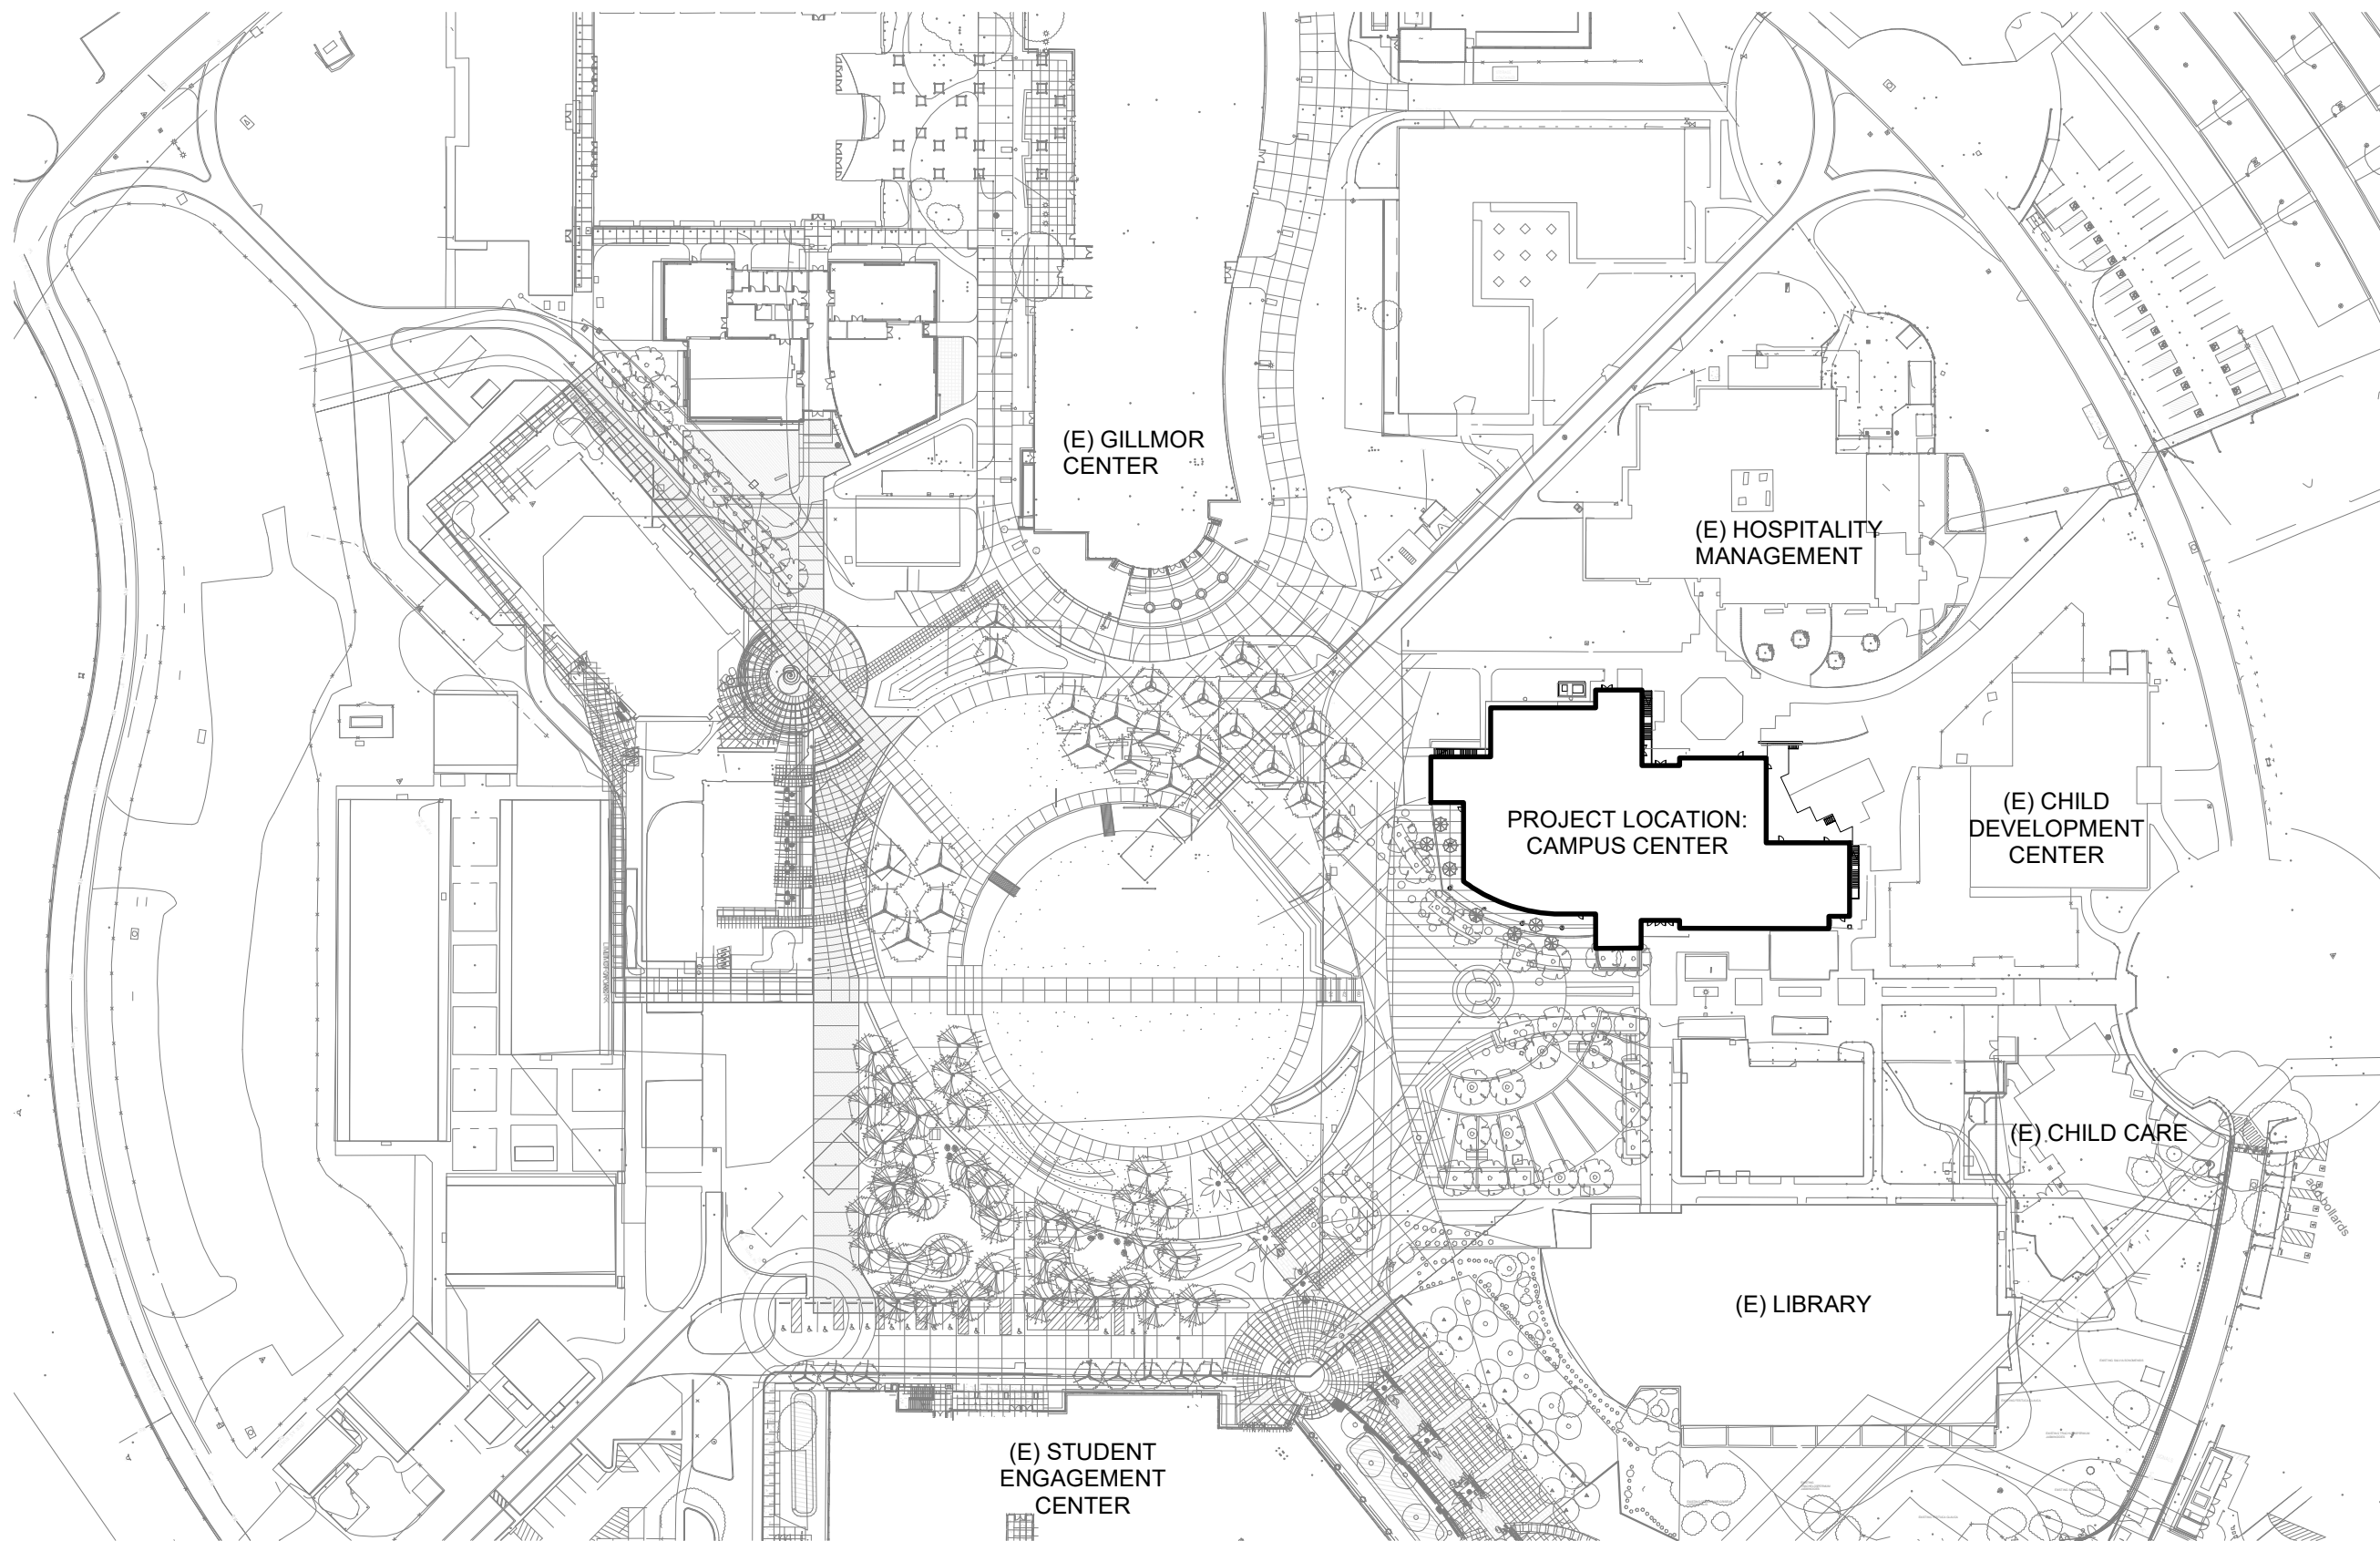

CAMPUS SITE PLAN

MISSION COLLEGE CAMPUS CENTER MAY 10, 2024



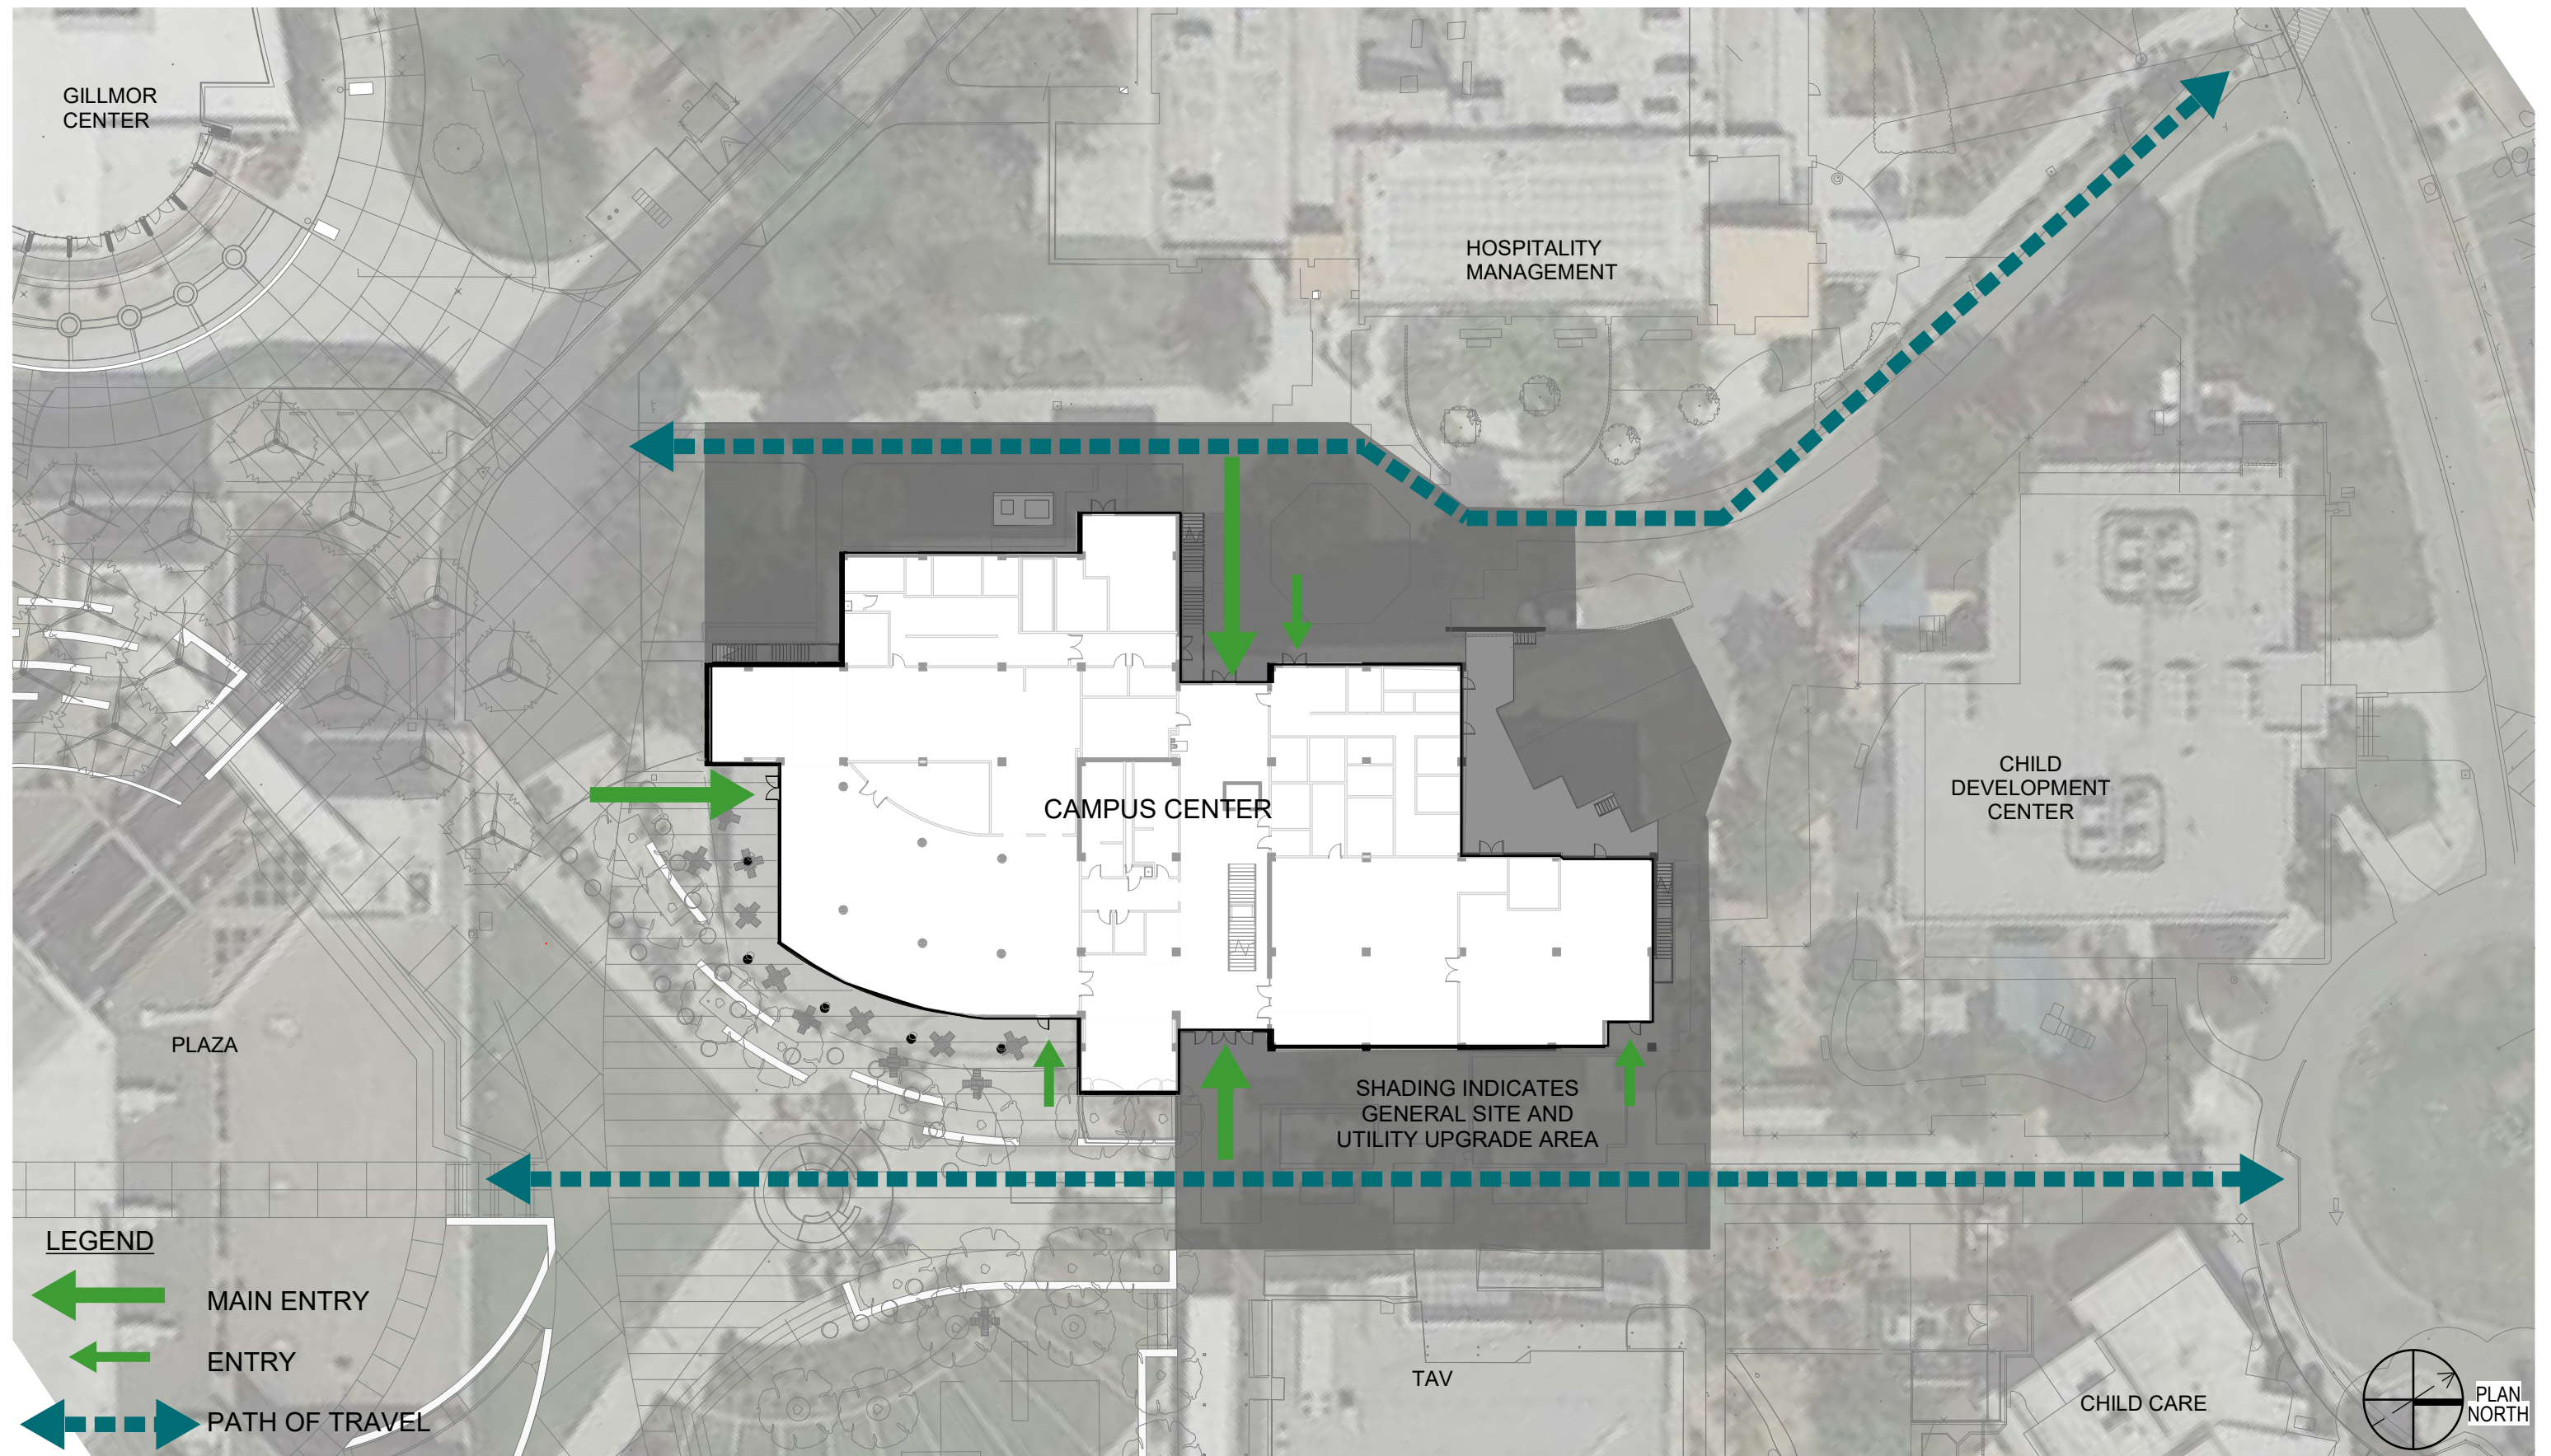


SITE PLAN

MISSION COLLEGE CAMPUS CENTER MAY 10, 2024







FIRST FLOOR PLAN

MISSION COLLEGE CAMPUS CENTER MAY 10, 2024

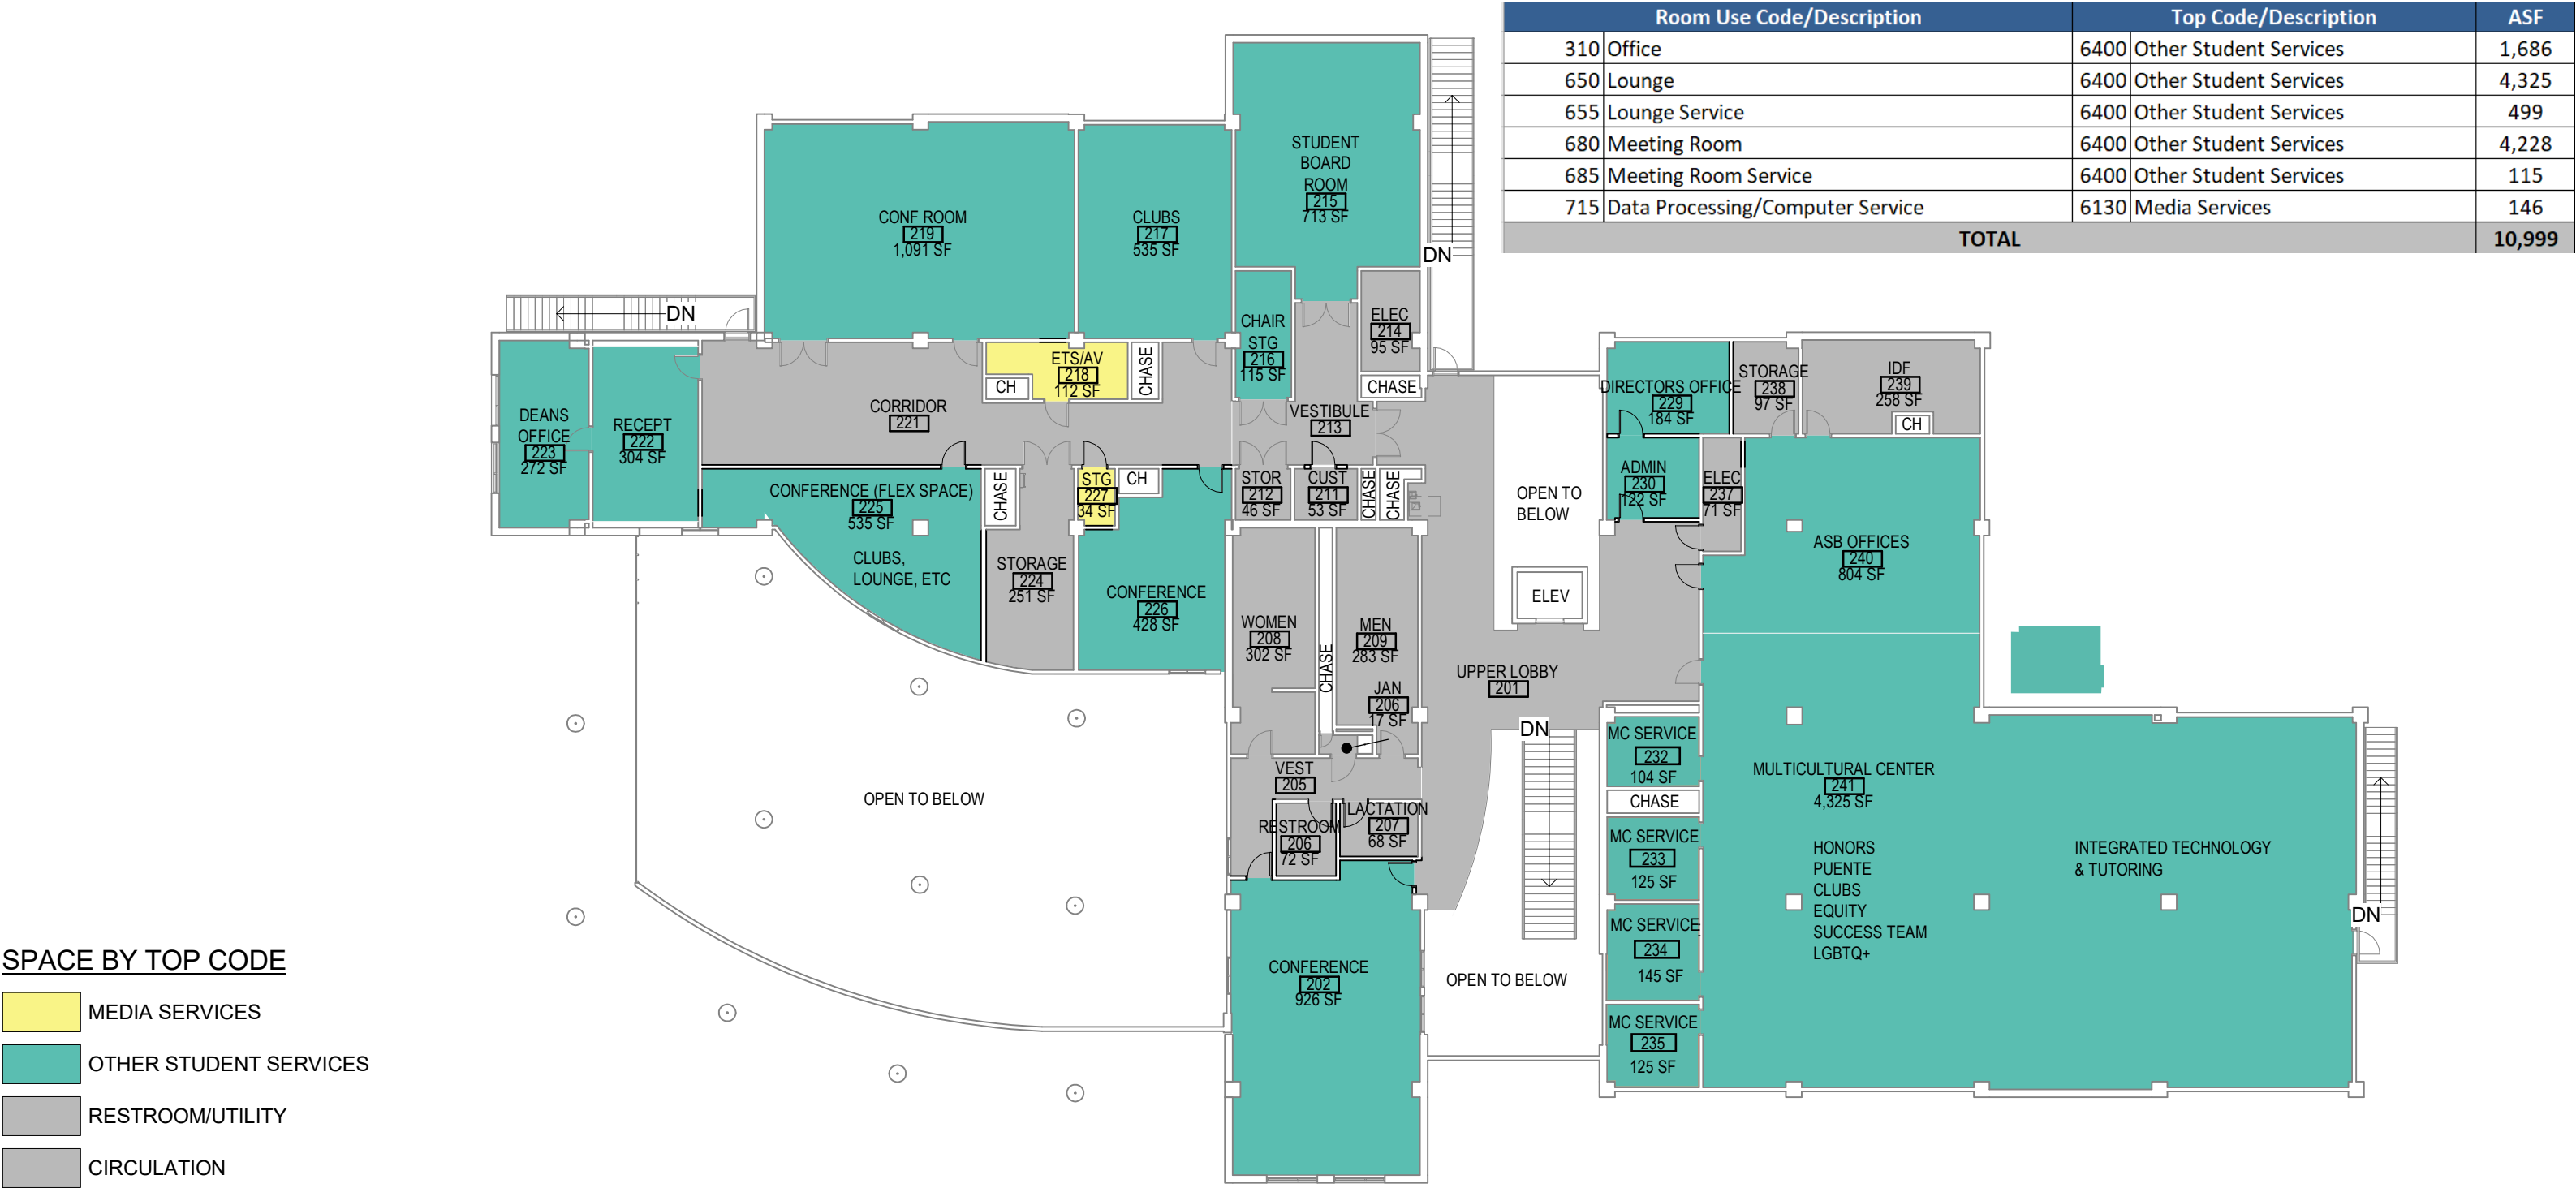

SECOND FLOOR PLAN

MISSION COLLEGE CAMPUS CENTER MAY 10, 2024

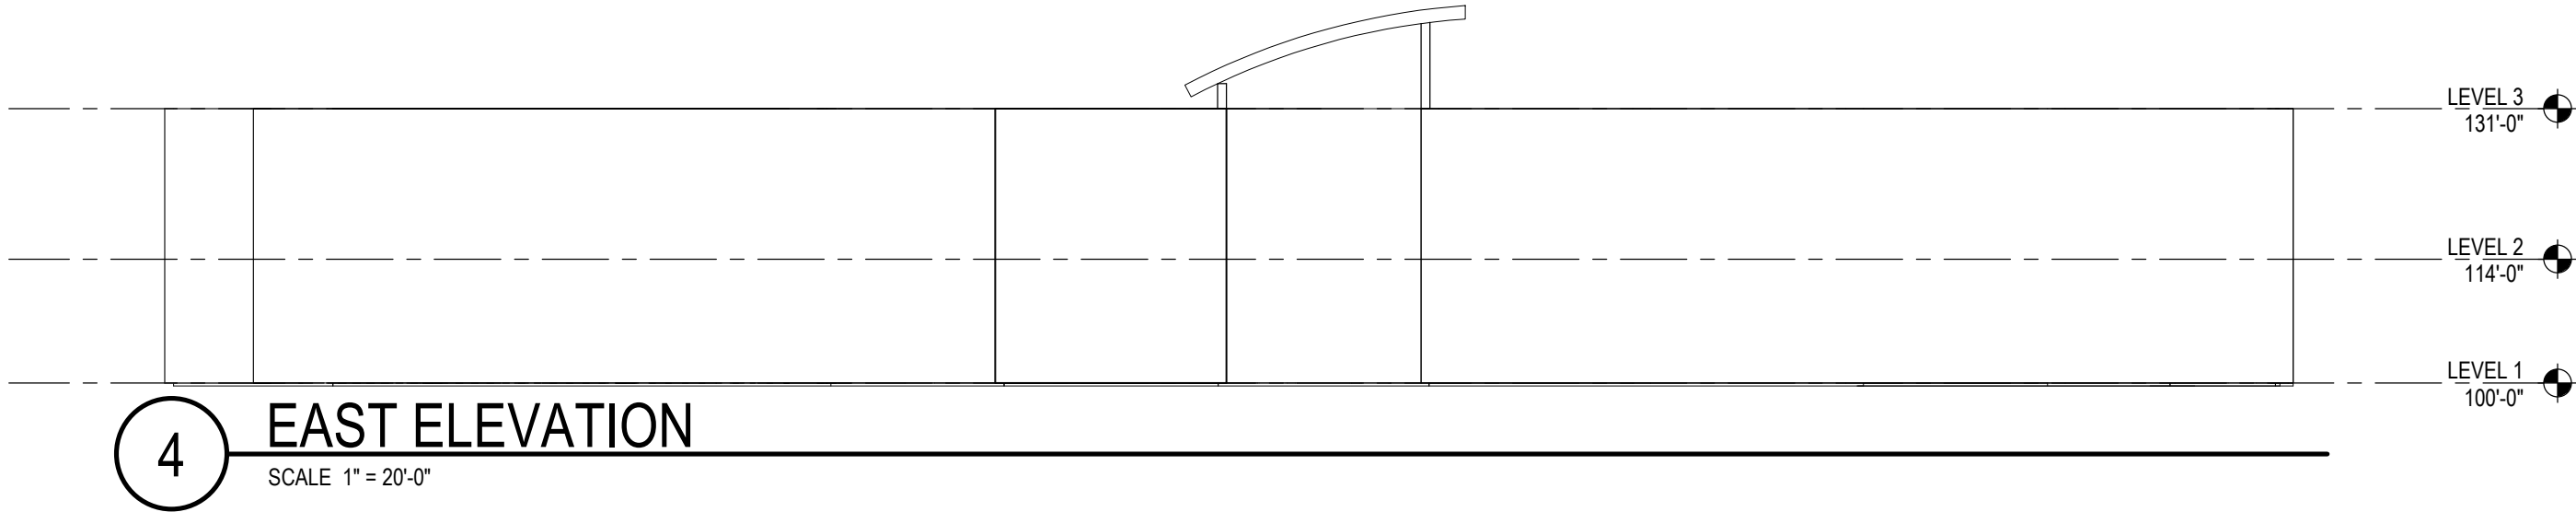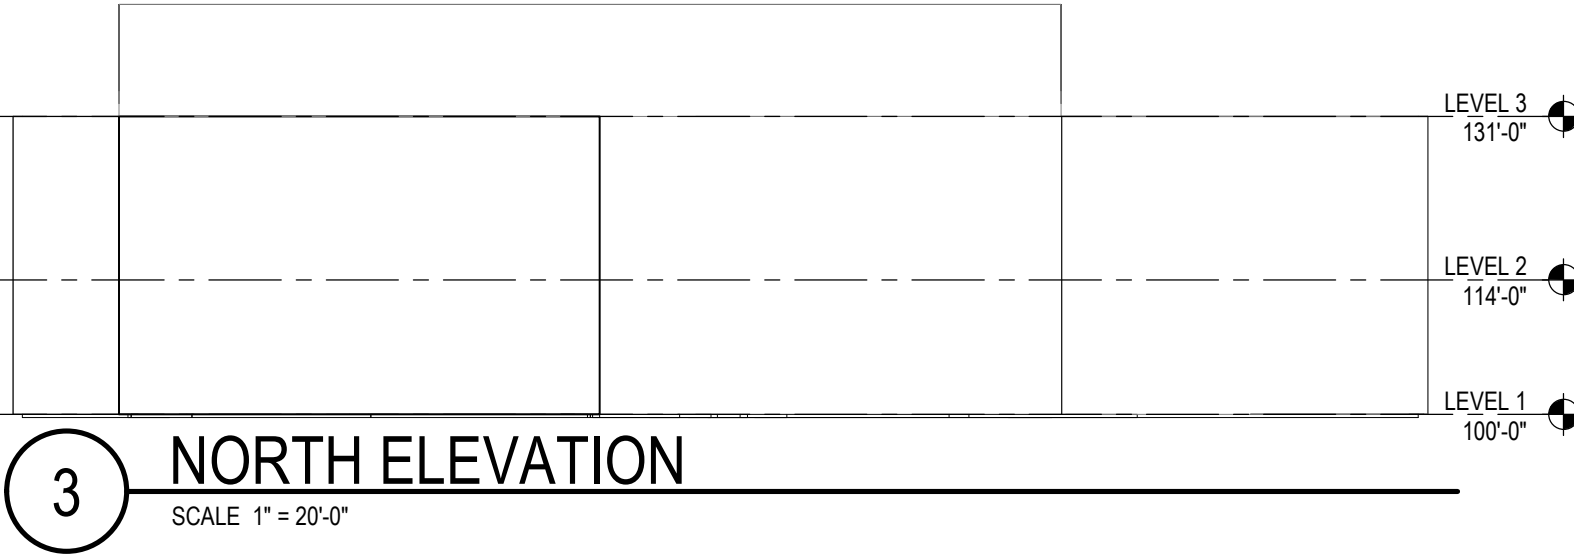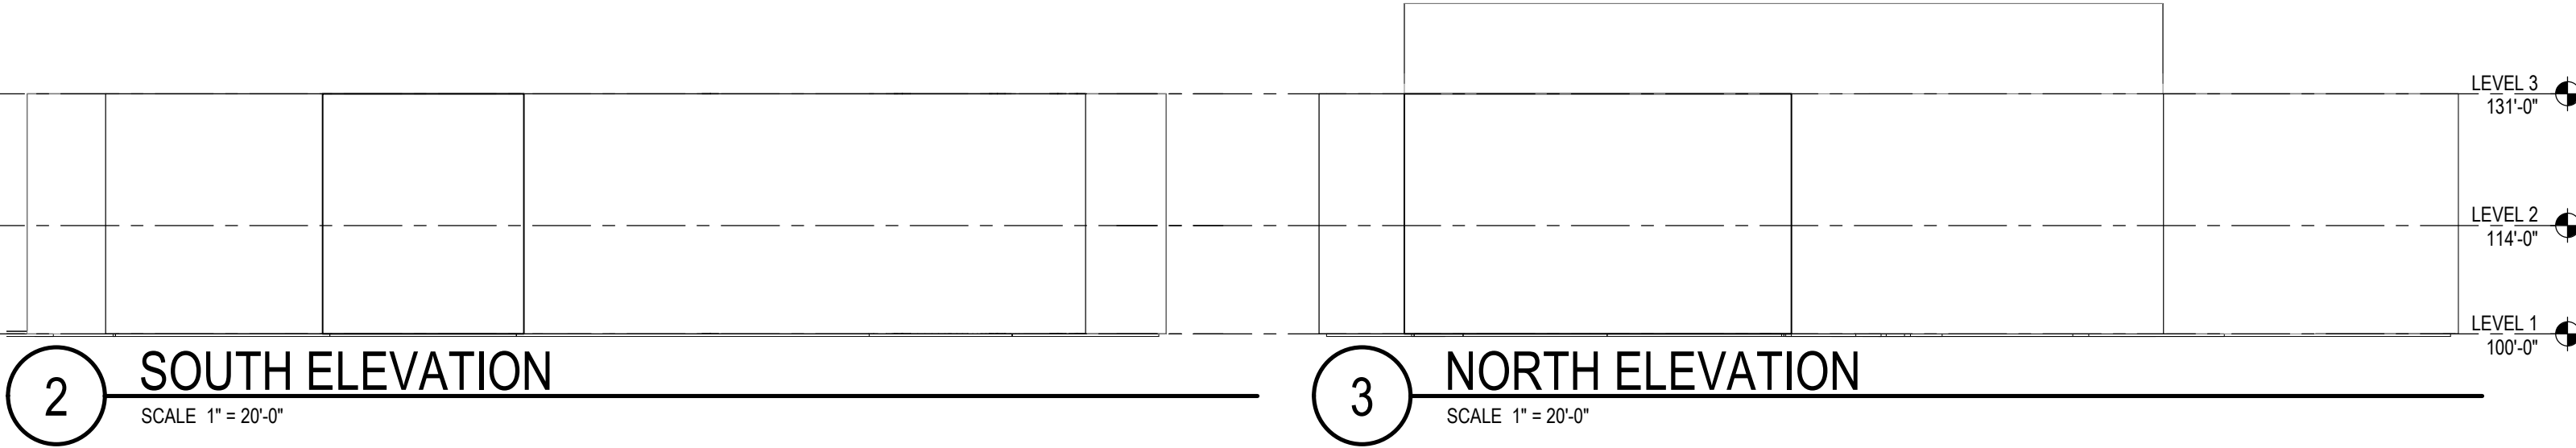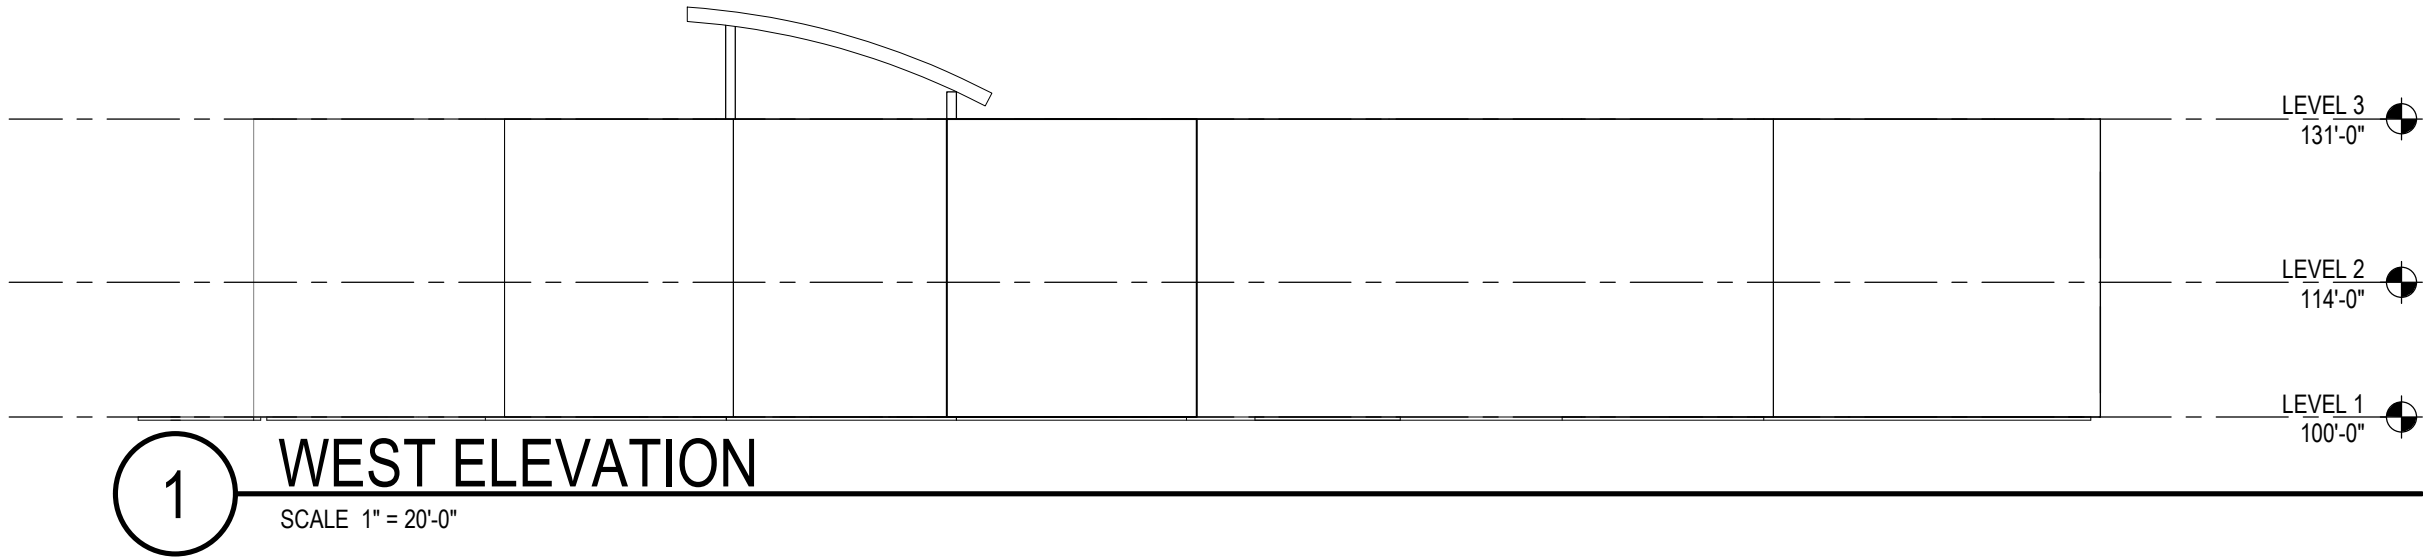

EXTERIOR ELEVATIONS

West Valley-Mission Community College District (490)
Mission College (492)
Project: Student Campus Center Renovation – EPI : 5455

Rm Type	Description	TOP Code	Department	ASF	Sec. ASF	Increase In Space	Equip. Cost/ASF	Total Allowable Cost
050	Inactive Area	6910	Bookstore	0	4,010	-4,010	\$0	\$0
220	Spec Class Lab	0700	Information Technology	0	580	-580	\$370.82	\$0
220	Spec Class Lab	0701	Information Technology, General	0	557	-557	\$370.82	\$0
310	Office	0099	General Assignment	0	4,215	-4,215	\$39.88	\$0
310	Office	0701	Information Technology, General	0	273	-273	\$39.88	\$0
310	Office	6400	Other Student Services	1,686	0	1,686	\$45.5	\$76,713
310	Office	6450	Student Personnel Administration	0	276	-276	\$45.5	\$0
310	Office	6499	Other Student Services	0	1,033	-1,033	\$45.5	\$0
310	Office	6770	Logistical Services	503	362	141	\$45.5	\$6,416
310	Office	6940	Food Services	132	135	-3	\$45.5	\$0
310	Office	6999	Other Ancillary Services	0	2,111	-2,111	\$45.5	\$0
315	Office Service	0701	Information Technology, General	0	143	-143	\$39.88	\$0
315	Office Service	6770	Logistical Services	366	495	-129	\$45.5	\$0
315	Office Service	6999	Other Ancillary Services	0	16	-16	\$45.5	\$0
410	Read/Study Room	6120	Library	0	46	-46	\$59.86	\$0
530	Audio/Visual, Radio, TV	6130	Media Services	0	25	-25	\$178.04	\$0
540	Clinic St Care	6310	Counseling Services	0	134	-134	\$0	\$0
615	Assembly Service	6999	Other Ancillary Services	0	327	-327	\$0	\$0
630	Food Facilities	6940	Food Services	5,613	5,246	367	\$53.93	\$19,792
635	Food Facilities Service	6940	Food Services	978	2,204	-1,226	\$53.93	\$0
650	Lounge	6400	Other Student Services	5,690	0	5,690	\$41.33	\$235,168
650	Lounge	6999	Other Ancillary Services	0	426	-426	\$41.33	\$0
655	Lounge Service	6999	Other Ancillary Services	499	0	499	\$41.33	\$20,624
660	Merchandise Facility	6910	Bookstore	1,919	0	1,919	\$0	\$0
665	Merchandise Facility Service	6910	Bookstore	161	0	161	\$0	\$0
670	Recreation	6960	Students and Co-curricular Activities	2,122	0	2,122	\$172.5	\$366,045
675	Recreation Service	6960	Students and Co-curricular Activities	210	0	210	\$172.5	\$36,225
680	Meeting Room	6400	Other Student Services	4,228	0	4,228	\$41.33	\$174,743
680	Meeting Room	6770	Logistical Services	258	0	258	\$41.33	\$10,663
680	Meeting Room	6999	Other Ancillary Services	0	2,335	-2,335	\$41.33	\$0

685	Meeting Room Service	6400	Other Student Services	115	0	115	\$41.33	\$4,753
685	Meeting Room Service	6999	Other Ancillary Services	0	120	-120	\$41.33	\$0
690	Locker Room	6770	Logistical Services	0	94	-94	\$17.39	\$0
690	Locker Room	6940	Food Services	0	51	-51	\$17.39	\$0
715	DP/Computer Service	6130	Media Services	146	0	146	\$370.82	\$54,140
715	DP/Computer Service	6770	Logistical Services	0	250	-250	\$370.82	\$0
TOTAL		-	-	24,626	25,464	-838	-	\$1,005,281

JUSTIFICATION FOR ADDITIONAL COSTS EXCEEDING GUIDELINES

☐ Construction (including Group I equipment), ☐ Equipment (Group II and Furniture)

District: West Valley Mission Community College District **College:** Mission College

Project: Student Campus Center Renovation

Please use this and additional pages or diagrams to explain and justify items of cost not easily explained on other forms. Examples of items needing justification: site improvements, unusual or high-cost construction methods, or items of equipment that exceed ASF cost guidelines. This form, when completed, supplements both the "Quantities and Unit Costs Supporting the JCAF 32" and the "Guidelines-based Group II Equipment Cost Estimate" forms.

The proposed scope of work includes reconstruction of 2,080 ASF of bookstore space which is recognized by the State and District to be a non-state supportable space without any state cost allowance. Thus, the District will be fully paying for all hard and soft project costs related to the reconstruction of Bookstore space within the Student Campus Center. The District estimates that the hard construction cost (not escalated to mid-point of construction) for non-state supportable Bookstore space within the building will be approximately \$1,376,960 (2,080 ASF x \$662/ASF = \$1,376,960).

Estimated hard construction costs for the proposed project exceed current state guidelines at CCI 9654. Current state guideline costs are not estimated to be sufficient to reconstruct the building ASF and GSF. Multiple factors may be contributing to costs exceeding state guidelines including, but not limited to, increases in the cost of raw construction materials, labor shortages, supply chain disruptions, higher than average inflation rates, and market uncertainty. The proposed project is estimated to exceed maximum state guidelines for hard construction (at CCI 9654) by \$2,613,245. These costs are directly related to hard construction of the building, including concrete, masonry, metals, wood/plastics, thermal/moisture protection, doors/windows, finishes, specialties, conveying systems, fire suppression, plumbing, HVAC, electrical, communications, and safety/security.

DETAILED EQUIPMENT LIST

College: Mission College

Project: Student Campus Center Renovation

Item #	Item Name ¹	Units	Cost per Unit	Total Cost
	List to be provided when the Plan Year of funding the equipment phase is due to FPU: • Traditional= due year after initial FPP submittal		\$	\$

¹Cost requests for equipment are to be limited to those required for new programs or for net expansion space in existing programs.
